

Change Management Toolkit



Change Management Toolkit v3



Who is it for?

The Toolkit is a resource for **anyone** involved in managing change, whether as a Programme, Project or Business Change Manager.

How should it be used?

The Toolkit details a framework for change which includes phases, associated tasks and activities for a change project, including the people side of change.

To access the tools and templates referenced in the toolkit you will need to be a member of the [FutureNHS Change Management Network](#).

Quick Start – Click below

Dive straight into the Toolkit

I am a **Change Manager**, wanting to gain new insights


I am a **Project Manager**, unsure of the change activities to make my project a success

I am **interested** in change management and just want to know more about it



Navigation

Navigation Buttons



Use the shortcuts to move quickly between phases.

Please note that the [Prev](#) (Previous Slide) button does not work in the PDF version of the Toolkit.

Navigating the content

Each section of the Toolkit describes a different Phase of a typical change project and contains the following information:

Phase Outputs


The intended outputs of the Phase

Key Activities

Key activities to include in the Phase

Please note - some tools and techniques appear in multiple phases because they are appropriate in different ways at different times.

Although the tool remains the same, the context in which it should be used is referenced in the appropriate phase.

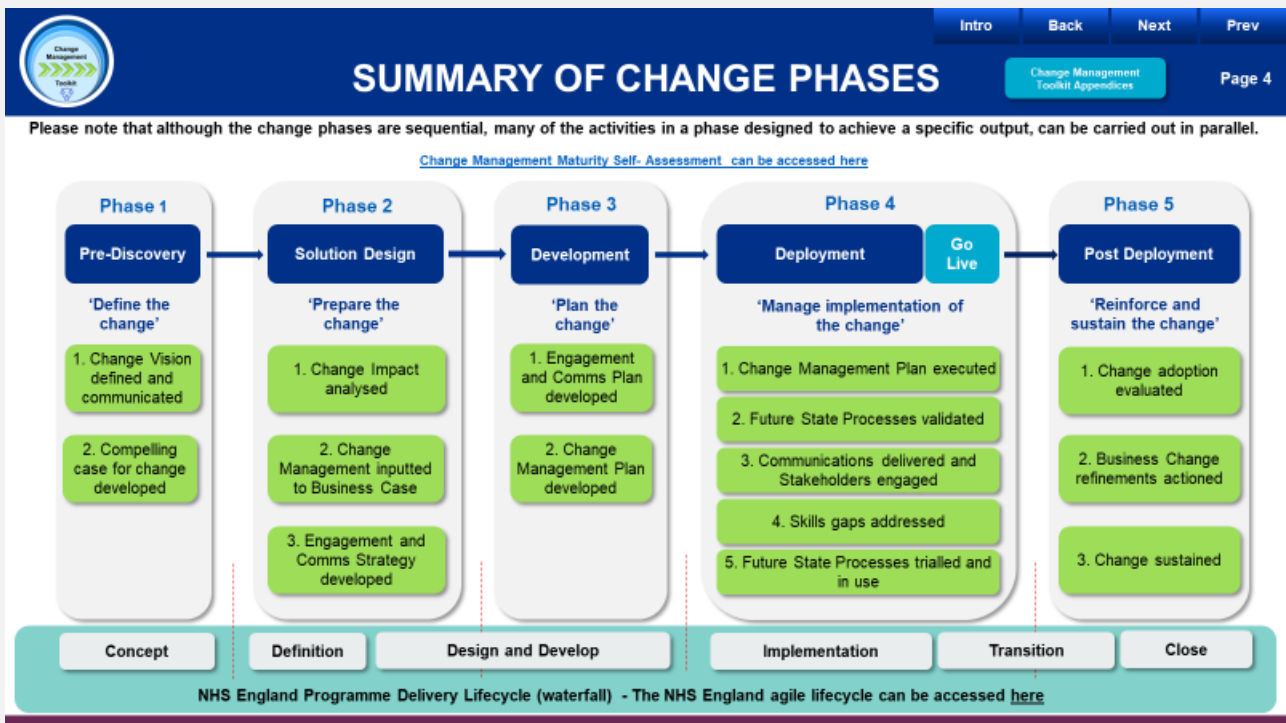




SUMMARY OF CHANGE PHASES

Please note that although the change phases are sequential, many of the activities in a phase designed to achieve a specific output, can be carried out in parallel.

[Change Management Maturity Self- Assessment](#) can be accessed [here](#)

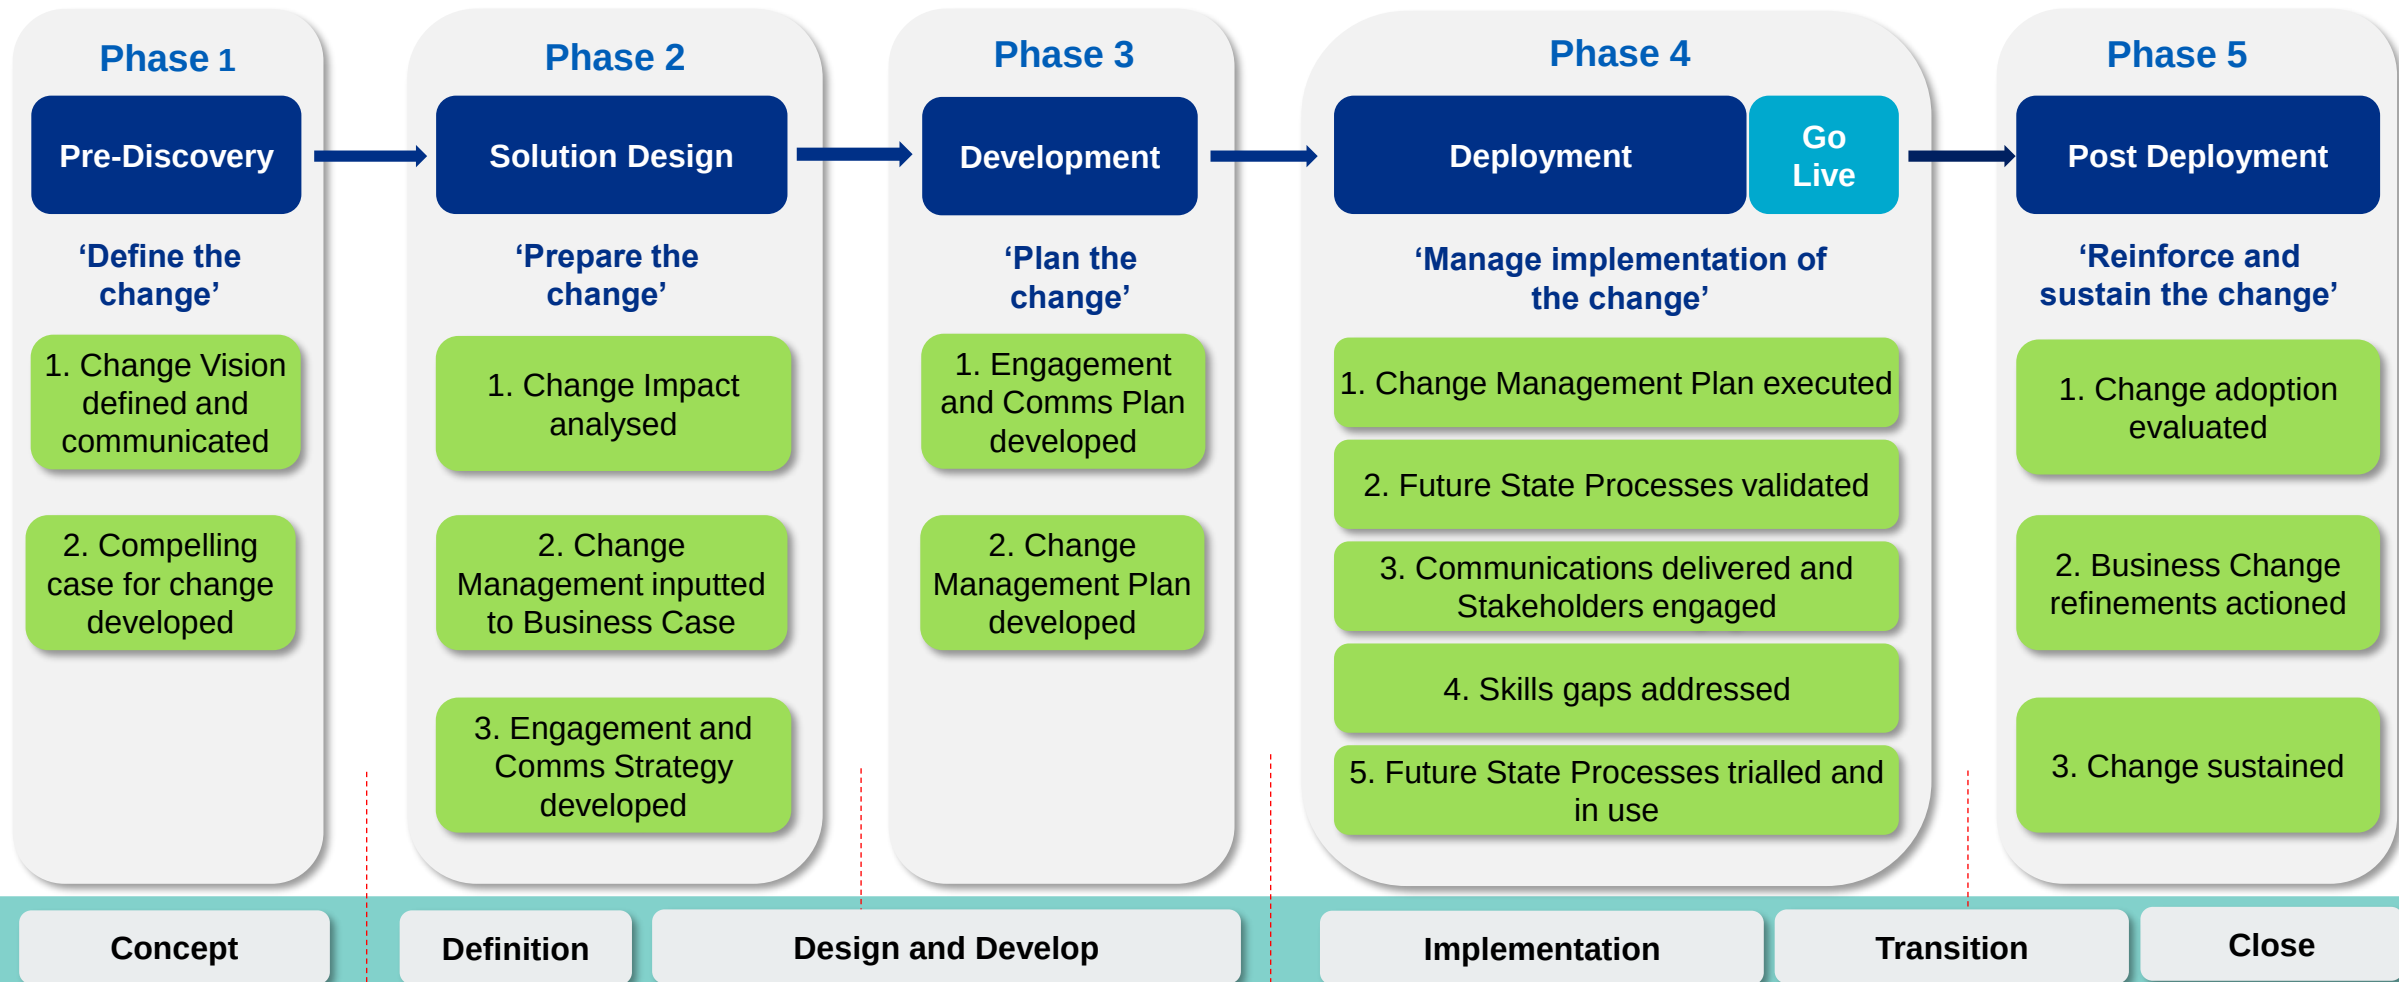

Phase 1: Pre-Discovery



Objective:

Define the Change



Outcome:

Engage early, build executive relationships, shape the programme and make an informed decision on change feasibility

Phase 1

Pre-Discovery

'Define the change'

1. Change Vision defined and communicated

2. Compelling case for change developed

PHASE OUTPUTS	KEY ACTIVITIES			
<u>Change Vision defined & communicated</u>	1. Commence Exec Engagement	2. Develop a stakeholder map, analyse and segment stakeholders	3. Define and communicate a clear vision for the future	
<u>Compelling case for change developed</u>	1. Undertake Situational Analysis (as-is)	2. Produce high level benefits	3. Identify drivers, risks and potential resistance	4. Evaluate appetite for change

Phase 1: Pre-Discovery

Change Vision defined & communicated

The change vision gives the organisation a picture of what the future looks like after the change is implemented.

It tells stakeholders why they should:

- let go of the past
- sacrifice and work hard in the present
- look to the future



Introduction

Defining a clear vision for change is essential, as this:

- Enables all those engaged in or affected by the change to understand its purpose and commit to the steps needed to make the change work

There are many methods and techniques that can be used to support this activity, some of the most widely used being:

- Soft systems methods (SSM)
- Mind maps and Whys, What's and How's
- Rich Pictures and Storytelling

Key Activities

1. Commence Exec Engagement

2. Develop a stakeholder map, analyse and segment stakeholders

3. Define and communicate a clear vision for the future



Additional Information

There is often confusion between the terms 'vision' and 'mission'. Both are relevant for change initiatives, but the focus for a change initiative is vision.

Stakeholders will have many different views and opinions about the vision and priorities for change, with some viewpoints conflicting, so it is important to reach a shared vision of what the business should be like in its 'future state'.



Phase 1: Pre-Discovery

Page 7

Key Activity

1. Commence Exec. Engagement

Change Vision defined & communicated



Additional Information

Build relationships with the relevant Execs (Trust Board, ICS Execs etc.) and influence the programme scope.

Build a network coalition of sponsors.

A strong sponsor network can be created by mapping out a change network . This network involves people from across the organisation, made up of Change Champions and Change Agents.


- Define a purpose for the change network and assess the requirements
- Collaborate with Project Sponsor to create Project Charter* and obtain go/no-go decision
- Set out expectations and responsibilities of the sponsor for each change phase

If the Project or Programme you're supporting has a Project/Programme Charter*, it can provide valuable input to this activity.

*A project charter is a formal short document that states a project exists and provides project managers with written authority to begin work. A project charter document describes a project to create a shared understanding of its goals, objectives and resource requirements before the project is scoped out in detail.

Tools and techniques that can support this activity


Sponsor Coalition Tool



What makes a good sponsor



Change Network



Prosci (2012) research identified that the greatest contributor to overall change management success was 'active and visible executive sponsorship.'

Kotter (2012), in stage 2 of his 8-stage approach 'Creating the guiding coalition' states that:

"The change-leading coalition needs to be characterised by trust and a common goal, and must contain people with strong positional power, appropriate and varied expertise, credibility across the organisation and effective leadership."



APMG The Effective Change Manager's Handbook:

What makes a good sponsor?

p. 51, Change Agent Networks p. 294 -296

[Building a change network](#)



Phase 1: Pre-Discovery

Page 8

Key Activity

2. Develop a stakeholder analysis map, analyse and segment stakeholders

Change Vision defined & communicated




Additional Information

Create a stakeholder map:


- Identify stakeholders: workshops, mind mapping and rapid listing are a useful way to identify stakeholders and discuss how they will be prioritised
- Categorise the stakeholders: Using segmentation such as Customer, Provider, Influencer and Governance (CPIG)
- Analyse the stakeholders: to establish the engagement level (Actively Engage, Manage Closely, Monitor, Keep Informed, Keep Satisfied), commitment and capability to make the change
- Engage with the stakeholders: identify and prioritise engagement activities according to their stakeholder mapping category
- Regularly review your stakeholders: as a change progresses, its scope may alter, meaning stakeholders become less relevant and lose interest or involvement and you will also need to monitor their commitment and capability as it changes

Tools and techniques that can support this activity

Stakeholder Analysis Tool



Engagement and Comms Strategy



Engagement and Comms Plan



Through understanding stakeholders, prioritising and mobilising them, Change Managers begin to gain and sustain the momentum for change.

The 7 principles of Stakeholder Engagement are a useful guide for managing stakeholders:

1. You can forget important stakeholders, but they won't forget you
2. Identification is a continuous practice – new stakeholders can emerge during change and old ones can fade away
3. Prioritisation and segmenting stakeholders is a moment in time. Regularly re-prioritise
4. Some stakeholders are best engaged by others
5. Seek first to understand, and then be understood.
6. Emotion trumps reason
7. Demonstration trumps argument



APMG The Effective Change Manager's Handbook, Stakeholder Strategy, p. 172-209, The 7 principles of stakeholder engagement, p. 174-208



[Stakeholder analysis](#)

Phase 1: Pre-Discovery

Page 9

Key Activity

3. Define and communicate a clear vision for the future

- Capture and select from a wide range of stakeholder viewpoints and perspectives to help build consensus using techniques such as 'Mind Maps'
- Select the most relevant and interesting viewpoints as the basis for defining vision using a 'why-what-how' hierarchy
- By applying [Systems Thinking](#) you can define a vision statement for the system you want. (Take into account the organisations mission, vision and core values)
- Create pictorial representations ('rich pictures') of a desired future state to help validate the vision with a wide variety of stakeholders



Change Vision defined & communicated

Tools and techniques that can support this activity


Mind Mapping



Rich picture & story telling



"Why-What-How" – Sinek's Golden Circle



Additional Information

The goal in communicating the change vision is to "make the complex appear simple".

Clear communication of the vision establishes the foundation for gaining commitment from stakeholders to embrace this new direction.

Simplicity and repetition of the change vision fosters understanding and retention.

Soft systems methods (SSM) provide a valuable tool set for capturing, exploring and selecting viewpoints. SSM helps to explore the different viewpoints of stakeholders, develop models of how things might work and understand the gap between the "future state" and the "current state" to identify "what needs to change".

At this early stage, the vision does not include future state processes, but is a representation of what the future will look like.



APMG The Effective Change Manager's Handbook,
Developing Vision, p.97-115
[Communicate the change vision](#)
[Simon Sinek Golden Circle](#)

Phase 1: Pre-Discovery

Compelling case for change developed

The case for change and desired outcomes can be used to engage employees and transmit to your stakeholders why they should invest in that effort required by the change.

Change initiatives need the commitment and motivation of the people who are receiving the change.

“Most people aren’t inspired by logic alone, but rather by the fundamental desire to contribute to a larger case. It can give greater meaning and purpose to your effort, extraordinary results are possible”

[John Kotter \(2018\)](#)




Introduction

The purpose of a case for change is to introduce the change and explain the following:

- To explain the reasons for the change including internal and external drivers.
- To highlight the expected benefits and desired outcomes. Also consider disbenefits and any risks.
- To demonstrate leadership support
- To provide a clear vision for success
- To tackle the [“What’s in it for me?”](#) questions.
- To minimise resistance to change
- To gain buy-in and support from internal and external stakeholders impacted by the change

Key Activities

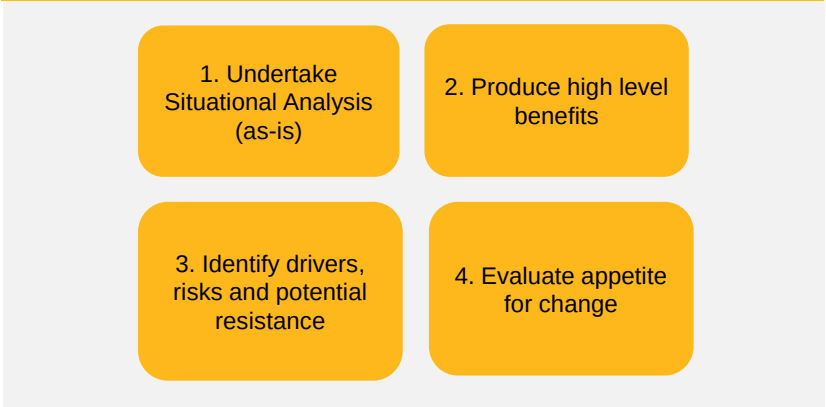

Additional Information

Anxiety and lack of understanding can cause resistance to change. The role of the Change Manager - during periods of anxiety and uncertainty - is to help people feel more in control of the situation.

A useful tool describing the forces that are acting for and against individuals is ‘The Change Formula’ (Beckhard and Harris, 1987)

$C = [ABD] > X$

C = Change

A = level of dissatisfaction with the status quo

B = desirability of the proposed change

D = practicality of the change (knowledge of the next practical steps, minimal risk and disruption)

X = perceived ‘cost’ of the change

An individual will decide to make the transition if they perceive that the effort or ‘cost’ of changing is worth it.

Phase 1: Pre-Discovery


Key Activity

1. Undertake Situational Analysis (as-is)

- Analyse the current state, how things are done today, what is not working well (or could be working better)?
- What are the signs that change is necessary?
- What are the consequences or risks of not changing?
- What is the urgency, how much time do we have to change? What do we need to start, stop or continue doing?
- Recommended tools for examining the present situation are; Porters ‘[Five Forces Model](#)’ at the industry level, a ‘[SWOT analysis](#)’ for comparison with competitors and you could revisit ‘Lewin’s [Force-field Analysis](#)’ for analysing driving and resisting forces.
- Begin defining the future state using information from the ‘Change Vision’ activities’. Think about the intended business outcomes and how you will know when you have reached the desired future state. Envisioning this future state will help the organisation to determine the extent of change required, resources required and the vision stakeholders will need to embrace.
- Use a tool such as a ‘[High level Gap analysis](#)’ to give an initial view of the scale of change required.

Compelling case for change developed

Tools and techniques that can support this activity

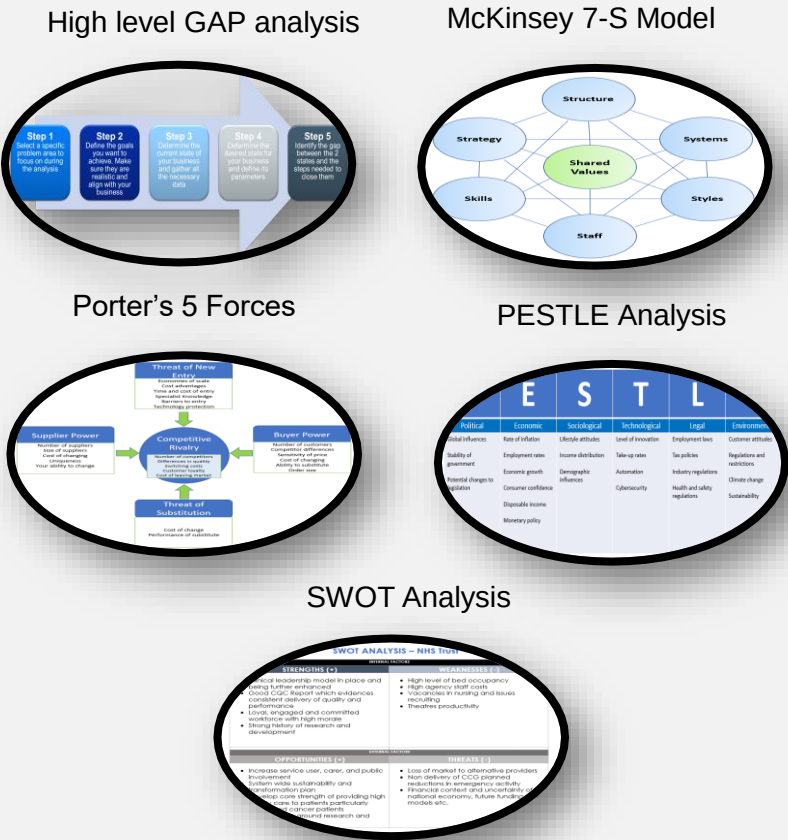

Additional Information

Before commencing a full gap analysis, you will need to spend some time mapping the current business processes, relationships and dependencies. This can be achieved by process mapping or Business Activity Models (BAMs) or a combination of both.

BAMs are ‘soft’ models that represent diagrammatic prototypes of a viable and complete ‘business system’ that shows how the future state described in the Business System Definition or Target Operating Model will operate.

The results of an initial gap analysis lays the foundations for a more in-depth specification of the change requirements.



APMG The Effective Change Manager’s Handbook, p. 92 - 93 120 – 131, p.262 – 264, p. 111 – 129



[Gap analysis](#)

Phase 1: Pre-Discovery

Page 12


Key Activity 2. Produce high-level benefits

- Identify the benefits and disbenefits, focusing primarily on benefits discovery workshops and benefits mapping
- Quantify the benefits, answering the 'how much?' question by accurately forecasting the scale of benefits anticipated
- The two steps above create a foundation for informed options analysis, investment appraisal, portfolio prioritization and the management of benefits realisation, which will be looked at in the next phases
- John Kotter (1996) argues that 70% of change initiatives fail, and attributes this to the fact that most organisations do not put in the necessary preparation or see the project through correctly. He outlines the Eight-Step Model which emphasises that change is not a simple and quick process. For benefits to be realised, the change should be made carefully


Compelling case for change developed

Tools and techniques that can support this activity

Benefits Map



Kotter's Eight-Step Model



Benefits Discovery Workshop



Additional Information

Benefits represent the rationale for investment in change initiatives. It is therefore crucial that benefits are managed efficiently and effectively.

The Change Manager:

- Has a crucial role in all of this – from identifying, quantifying and agreeing benefits through effective planning, to their realisation, reporting, capturing and disseminating lessons learned.
- Acts as a bridge between the change initiative and the business areas impacted by the change
- Liaises with the business and operational areas throughout the change process to ensure a continued focus on benefits

Whilst the focus should be to 'start with the end in mind', benefits and disbenefits identification and quantification should be started as early as possible in the business change lifecycle.

If you want training on how to do a Benefits discovery workshop (book onto the training and view videos)
<https://future.nhs.uk/NationalBenefitsManagement/grouphome>



APMG The Effective Change Manager's Handbook, p. 120 – 131, p.135, p.262 – 264, p. 111 – 129

[Gap analysis](#)

[NHS Quality Improvement](#)

[Benefits Management Training](#)



Phase 1: Pre-Discovery

Page 13

Key Activity

3. Identify drivers, risks and potential resistance

- Identify the drivers of change, the factors driving the need to change. This information can maintain the strategic focus and energy throughout the change
- Understand the restraining forces that make the change more difficult
- When considering the [case for change](#), a very useful tool is the 'Force-Field Analysis' which can help assess the impact of driving forces versus restraining forces of the change and give an indicator of the likely success of the change initiative
- Put an action plan in place to augment the driving forces and/or reduce the restraining forces.
- Use Bridges' Transition Model to identify and understand the emotional journey employees will encounter during the change
- You can apply the [Edgar Schein model](#) to help explain the impact of an organisations culture.

The model consists of three layers:

- Artifacts and behaviours
- Espoused values
- Basic underlying assumptions


Compelling case for change developed

Tools and techniques that can support this activity


Force-Field Analysis




Leverage




Risk Assessment



Bridges' Transition Model



Case for Change




Edgar Schein Model



Additional Information

Kurt Lewin's Force Field Analysis (1951) is based upon Lewin's opinion that 'an issue is held in balance by the interaction of two opposing sets of forces: those seeking to promote change (driving forces) and those attempting to maintain the status quo (restraining or resisting forces).' If an organisation desires to make change quickly, either the driving forces need to be augmented or the restraining forces decreased. Ideally, both of these must happen.

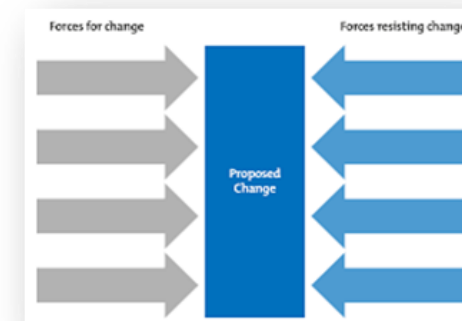

APMG The Effective Change Manager's Handbook, Force field analysis p. 93
[Making a compelling case for change](#)

Phase 1: Pre-Discovery

Page 14

Key Activity


4. Evaluate appetite for change

- The business needs to understand the full implications of the changes it has to make, in terms of the full range of 'capability' required in the future state. To support this, carry out an analysis of capability looking at: knowledge and information, organisation and people, process and procedure and environment and infrastructure
- An important step for a Change Manager is making a case for the importance of managing the people side of change. This can be addressed to various groups including project teams, senior leaders, middle managers or supervisors in order to connect Change Management to what matters to them (e.g. meeting financial objectives for senior leaders)
- Provide knowledge, training, tools and coaching in order to help the impacted people build their Change Management competency
- Apply Change Management principles to engage the roles involved


Compelling case for change developed

Tools and techniques that can support this activity

Change Management Capability Review (KOPE)



Systems Thinking



Additional Information

Remember you are defining 'future state' capability and not what you currently do.

Using the KOPE (**K**nowledge & **I**nformation, **O**rganisation & **P**eople, **P**rocesses and **P**rocedures, **E**nvironment & **I**nfrastucture) model helps the full implication of the change to be understood.

Understanding the full implications of change enables a fully informed decision process about where developments or investment are needed.

The KOPE capability analysis also provides the baseline against which specified improvements can be measured, post implementation



APMG The Effective Change Manager's Handbook, capability analysis p. 116 – 120



[Capability analysis](#)

Phase 2: Solution Design

Objective:
Prepare the change

Outcome:
A blueprint for the implementation...the means by which we move from the current state to the future state

Phase 2

Solution Design

'Prepare the change'

1. Change Impact analysed

2. Change Management inputted to Business Case

3. Engagement and Comms Strategy developed

PHASE OUTPUTS	KEY ACTIVITIES					
<u>Change Impact analysed</u>	1. Produce Change Impact Assessment	2. Perform Detailed GAP Analysis	3. Perform Initial Skills Gap Analysis	4. Commence Detailed Benefits and Disbenefits	5. Undertake Initial Risk Assessment	6. Evaluate Organisational Impact
<u>Change Management inputted to Business Case</u>	1. Create Outline Change Management Plan					
<u>Engagement and Communications Strategy developed</u>	1. Develop and Refine Engagement and Comms Approach	2. Manage Attitudes to Change	3. Define the Governance, Roles and Change Responsibilities of Stakeholders			

Outcomes:

Phase 2: Solution Design

Change Impact analysed

The impact analysis helps to understand the impact of the change on individuals, teams, business units and the organisation.



Identifying and analysing the impact of change is one of the keys to effective change management planning and helps to avoid and minimise the disruptive effects, while supporting positive aspects of change.

Introduction

- The purpose of an impact analysis is to:
- Highlight the impact on the ‘business as usual’ aspect of the organisation
- Explore the impact of change and how this will affect individuals, teams, business units, the organisation, customers and stakeholders
- Minimise the disturbance and turbulence caused by the change
- Manage ongoing risk during change
- Help maximise the benefits of change
- Highlight and manage any risks that may occur as a result of the change

Key Activities

1. Produce Change Impact Assessment

2. Perform Detailed GAP Analysis

3. Perform Initial Skills Gap Analysis

4. Commence Detailed Benefits and Disbenefits

5. Undertake Initial Risk Assessment

6. Evaluate Organisational Impact



Additional Information

Remember, if the change initiative is going to be costly, and with the potential to realise benefits, then there is more likelihood of causing a lot of disruption to business-as-usual operations. Therefore, always ask the question: “Why spend all this money if there won’t be any change?”



APMG The Effective Change Manager’s Handbook: Impact Analysis p. 268 to p.289



[Understanding the Impact of Change Management](#)

Phase 2: Solution Design

Key Activity

1. Produce Change Impact Assessment

Identify and understand the impacts of change and its effects on productivity, individuals, teams, customers and stakeholders

When identifying the impact of change, you should consider:

- **The intended changes:** the vision for the new world, the removal of barriers to get there, and the disruptions to productivity, individuals, teams, customers and stakeholders while implementing change
- **The unintended and/or unplanned outcomes:** any unforeseen circumstances that could cause issues and problems that could have a negative effect on productivity, individuals, teams, customers and stakeholders while implementing change
- **The change management activities:** what actions need to be taken to implement change, how this will impact 'business as usual' and productivity. You may wish to include the involvement of subject matter experts to help implement and manage change

Change impact analysed

Tools and techniques that can support this activity

Impact Analysis



Change Impact Assessment



Additional Information

Make sure that you consider the impact of change across the organisation as a whole, not just the areas that are directly impacted.

To calculate a change score, consider

- How complex is the process?
- How far away from their current process is the new process?

To calculate a readiness score, consider

- What is their attitude towards the change?
- Are the conditions right?
- What resources are available to make the change happen?
- Is there a change network established in the area?

Then consider the number of people impacted to determine where the majority of change needs to occur.



APMG The Effective Change Manager's Handbook, capability analysis p. 116 – 120



[Capability analysis](#)


Phase 2: Solution Design

Page 18

Key Activity

2. Perform Detailed GAP Analysis

Use process mapping to help highlight any areas of the organisation that would benefit from change initiatives.




- Produce a high-level review of the organisation's starting point (current state or as-is state) and end point (future state or to-be state). This will allow you to identify the change gap
- Identify the possible issues and barriers to change
- Explore possible change activities that could be implemented to help resolve any identified issues


Change impact analysed

Tools and techniques that can support this activity

McKinsey 7-S Model



Process Mapping – As-Is & To-Be with examples



Additional Information

Remember, the end goal/future state and the respective scope of the change should be carefully defined. Any mistake in doing so might turn the analysis in a completely different direction.

The standard Business Process Model and Notation (BPMN) can provide an understanding of business procedures in a graphical notation, allowing easy communication of complex ideas.



APMG The Effective Change Manager's Handbook: p 262 to 264



[BPMN Specification - Business Process Model and Notation](#)

Phase 2: Solution Design

Key Activity

3. Perform Initial Skills Gap Analysis

It's helpful at this stage to consider the skills gap that is likely to exist when people move from the current process to their future state.

A skills gap analysis is an assessment of the difference (or gap) between the current skills and the future skills required by stakeholders. To identify the skills gap, training colleagues will consider the information provided in the change impact assessment and carry out a training impact assessment and future Learning Needs Analysis (LNA also known as Training Needs Analysis or TNA).

A training impact assessment will be used before planning training to determine, at a high level, what the costs and resources for a training programme or initiative might be.

LNA is a process that identifies current skills, knowledge and attitudes in relation to current and anticipated gaps in training and development needs.


Change impact analysed

Tools and techniques that can support this activity

Learning Needs Analysis



Training Impact Assessment



The Why Training Matters Toolkit



Additional Information

It is also important to consider the wider impact of any training or development initiative associated with the change at this early stage.

NHS England has produced [The Why Training Matters toolkit](#) that considers a wide training landscape, focusing on five themes:-

- Define
- Measure
- Justify
- Improve
- Promote

Most change initiatives will consider the first two of these in detail.



APMG The Effective Change Manager's Handbook: p385-394



[Identifying Learning & Development Needs](#)

Phase 2: Solution Design

Key Activity

4. Commence Detailed Benefits and Disbenefits

Benefits management seeks to optimise benefits realisation by ensuring:

- Forecast benefits are complete and realistic
- Forecast benefits are realised in practice by ensuring that the required enablers, business and behavioural changes are in place
- Benefits are realised as early as possible and are sustained for as long as possible
- Emergent benefits are captured and leveraged and any disbenefits are minimised

The above can be demonstrated not just as part of the framework of accountability, but also to ensure the organisation learns ‘what works’ as a basis for continuous improvement

Change impact analysed

Tools and techniques that can support this activity

Benefits Discovery Workshop



Additional Information

Identifying the dependencies between benefits, changes and enablers can help with prioritisation and scope. This supports making decisions about what functionality or changes are no longer relevant for the business.

- Ensure benefits realisation management is embedded in the heart of the change initiative
- Ensure you get representative involvement from key stakeholder group



APMG The Effective Change Manager’s Handbook: p.132 to p.171



[Benefits Management Lifecycle](#)

Phase 2: Solution Design

Key Activity

5. Undertake Initial Risk Assessment


- Identify the potential risks and assess them using a 'Risk Analysis'
- Change risk should be looked at from 3 perspectives: Strategic, Business and Programme/Project
- Agree on actions that will manage or mitigate the risk effectively
- The actions will then need to be planned and implemented
- A 'risk register' is used to formally monitor, update on and report progress to your senior leadership
- Communicate the risks of your change initiative, providing status updates to project steering committees/senior leadership
- It provides an indication of how well the programme/project and the change are progressing

Another useful tool is the "Sustainability Risk Assessment" which highlights the top three risks or issues that will prevent the change from sticking or staying stuck

Change impact analysed

Tools and techniques that can support this activity

Risk Analysis/ Assessment



Change	Risk ID	Issue/Barrier/Risk Description	Probability	Impact	Overall
Strategic	SR01	That change impacts particularly culture	High	Negative	High
Business	BR02	Pressure to meet quality standards without any new external funding	Medium	Low	Medium
Programme/Project	PR03	Project completion not needed or not well defined	Low	Low	Low
Overall		Level of communication covering that it is fully understood	Low	Low	Low

Sustainability Risk Assessment



Change	Strategic	Business	Programme/Project	Overall
Strategic	High	Medium	Low	High
Business	Medium	High	Low	Medium
Programme/Project	Low	Low	High	Low
Overall	High	Medium	Low	High



Additional Information

The key words in risk management are:

- Proactive
- Management
- Accommodate
- Acceptably
- Professional
- Possibility

“Risk management is the sum of all proactive management directed activities within a project or change initiative that are intended to acceptably accommodate the possibility of failures in the elements of any change.”

[Paul Bower, ProjectSmart.co.uk](#)



APMG The Effective Change Manager's Handbook: Assessing and managing the risks of change, p.279 to p.285



[What is risk management?](#)

Phase 2: Solution Design

Key Activity
6. Evaluate Organisational Impact

We have already looked at how we can use the McKinsey 7s model to assess the impact of the change on various internal aspects of an organisation.

It is also important to look at what else is going on in the organisation and consider ‘other’ change and business-as-usual activities that may be happening across the organisation, such as:


- conferences
- holiday periods
- business year-end

Organisational heat maps are useful tools to assess the impact of various current change initiatives on the teams/departments throughout the organisation. This will give a better view of how much stress the organisation is under due to competing priorities.

Change impact analysed

Tools and techniques that can support this activity

Heat Map



Change Impact Assessment



Proof of Concept



Additional Information

It’s possible that a proof of concept (POC) is available for the programme.
If so, it’s really usefull to engage with POC activities to understand further the impact on the organisation.




APMG The Effective Change Manager’s Handbook: Change Impact P275-276
[Creating a heat map in Excel](#)

Phase 2: Solution Design

Change Management Inputted to Business Case

Throughout the life of a change initiative, Change Managers and project managers will need to work together to ensure that the two disciplines are in step.



This includes the Outline Business Case (OBC), which is a project document that captures the reason for initiating a project and helps convince a decision-maker to take action.

Introduction

The Change Manager is involved in ensuring the Outline Business Case (OBC) details the change methodology and appropriate [strategy](#) that will be used.

Change needs to be managed and embraced by individuals within the organisation, hence the need for a change management:

- [Strategy](#) - linked to benefits realisation
- Framework - to manage anticipated and unexpected change
- [Plan](#) - to explain what will be delivered by whom and by when in terms of activities

The methodology and strategy will vary according to the nature of the change. For example, a small change to a process or a complete transformation of the business will require different activities and hence change management methodologies.


Key Activities

1. Create Outline Change Management Plan



Additional Information

Change management should begin as early as possible in the change process in order to minimise the risks of misunderstanding and the resulting filling of gaps with ‘rumour’ or ‘through the grapevine’ discussions



APMG The Effective Change Manager’s Handbook: p. 310



[The Green Book and accompanying guidance and documents](#)

[Developing a project business case](#)

Phase 2: Solution Design

Key Activity

1. Create Outline Change Management Plan

At this stage an outline [Change Management Plan](#) needs to be developed to help manage the change process and the tasks and activities required.

A typical plan will include Engagement and Communications, Sponsor Roadmap, Training, Coaching, Implementation, [Resistance management](#) and [Transition management](#).

You have built on work carried out in pre-discovery. Look now to establish a [Change Network](#). By this stage the purpose of the network - and what the members of the network will actually do - should be adequately mapped out.

Selection of members and a kick-off/training session should commence. Agree ways of working, collaboration methods and then plan to launch the network.


Use [Bridges' Transition Model](#) to build strategies for helping people to let go of the 'old ways', helping them to make the journey and encouraging commitment to a new future

There also comes a point (Tipping Point and Critical Mass) at which during planning and transition that the change manager feels the full force of [resistance](#) in all its forms. That groundwork for change adoption has been done at that point - it starts to feel easier, no longer requiring specific attention to make it stick!


Change Management Inputted to Business Case

Tools and techniques that can support this activity


Tipping Point and Critical Mass




Change Network




Resistance Management Plan



Change Management Plan



Bridges' Transition Model



Additional Information

Throughout a project, [Change Management Plan](#) will be 'progressively elaborated' as new information becomes available or new levels of task detail are developed.

It will be continually refined, revised and updated to reflect current and expected progress.

A transition plan is a necessary component of a [Change Management Plan](#) as we need to manage both the change and the transition. Monitor transition issues and peoples response to the change and implement strategies to help people with the transition.



APMG The Effective Change Manager's Handbook: p. 310 and p.358 (Tipping Point) p.474-475




[Change management methodology](#)

Phase 2: Solution Design

Engagement & Communications Strategy developed

An Engagement and Communications Strategy is a written document that describes who and how the Change Manager will engage. This will contain an element of 'comms' but should include a range of activities to ensure wider engagement as well as information dissemination.



The purpose of communicating change is to:

- Build awareness of the need for change
- Achieve a shared understanding of what is required across stakeholder groups
- Gain commitment and get people actively engaged

Introduction

People process information in different ways so you need to consider different types of engagement and communications activities as well as the style and formats used to help overcome people’s natural resistance to change.

It is important to appeal to ‘hearts and minds’ to make an emotional connection that helps achieve fuller engagement and reduces resistance.

Regular monitoring and evaluation of engagement and communications effectiveness is essential. Decisions can then be made about actions to ensure engagement and comms objectives are being met and further developments made.

Key Activities

1. Develop and Refine Engagement and Comms Approach
2. Managing Attitudes to Change
3. Define the Governance, Roles and Change Responsibilities of Stakeholders

Additional Information

Regular communication keeps people updated on progress and helps to manage rumours.

If you don’t tell them, people will fill in the gaps in your communications themselves.

It is better to say, “We do not know yet and here is what we are doing to find out.”

To accommodate the needs of diverse groups, different types of engagement and communications activities and interventions should be considered.

People have different preferences for the way they process information, so the same messages need to be conveyed using different formats and styles.

You can also consider using Nudge theory to support your development of your engagement and communications activity to ensure that you are encouraging people to make the choices that will best support the change initiative.

APMG The Effective Change Manager’s Handbook: Communicating Change P221 – 233

[Change Management and Communication Strategy](#)

[Nudge Theory Explained](#)

Phase 2: Solution Design

Key Activity

1. Develop and Refine Engagement and Comms approach

Setting out a well-considered engagement and communications plan will ensure that timely, appropriate and consistent activity takes place to deliver all the objectives set out in the [strategy](#). It shows who is going to deliver what, when, to whom and how that will be measured, by setting out:

- Target audience
- The objective that is to be achieved for that audience
- The key messages to communicate
- The activity that will deliver those messages and achieve that objective
- The timing of activities
- How the activity will be measured

The outputs from monitoring and evaluating your plan are invaluable during the change process. This information will highlight where communications have been fully understood, whether those affected are becoming fully engaged in the process and where collaboration is making the best contribution. The plan can then be reviewed as required.

[Nudge Theory](#) is based upon the idea that by shaping the environment, also known as the choice architecture, one can influence the likelihood that one option is chosen over another by individuals. A key factor of Nudge Theory is the ability for an individual to maintain freedom of choice and to feel in control of the decisions they make.

Engagement & Communications Strategy developed

Tools and techniques that can support this activity



Additional Information

Ensure your plan:

- helps people see where they fit and provides answers to their concerns: "[What does this mean for me and what do I need to do?](#)"
- supports the behavior change with engagement and communications that give stakeholders the information they need *when* they need it and equips leaders to help in the process.
- aligns closely with the business objectives for the change. Explain them in a story/ graphic to help everyone connect with the vision.
- includes core messages explaining the overarching change and vision as audience-specific messages to support key milestones.



APMG The Effective Change Manager's Handbook:
P- 251-255



- [Change Management Communication - David Grossman 2022](#)
- [Communications Planning](#)
- [Nudge Theory](#)

Phase 2: Solution Design

Key Activity
2. Managing Attitudes to Change

An emotional connection helps achieve fuller engagement during change so it is important to appeal to ‘hearts and minds’.

The Attitude to Change helps you see where to concentrate engagement and communications.

The Kubler-Ross model (The Change Curve) helps track the emotional states of individuals and groups as they navigate a non-negotiable change.




Where managers have already gone through the curve and cannot understand why others are still struggling to hear communications from others further down the acceptance route, a good tool is ‘Mapping Emotional States’. It can help in managing engagement and where to target specific communication activities.

Engagement & Communications
Strategy developed

Tools and techniques that
can support this activity


Managing emotional states



Attitudes to change



The Kubler-Ross Change Curve



Additional Information

Find multiple ways to communicate the key messages, so these can be repeated and have a better chance of being received.

Including face-to-face discussions as part of the engagement and communications approach is an excellent way to gather feedback and address any concerns and mis-understandings. These may take place in person or using virtual meetings software, such as Microsoft Teams or Zoom.



APMG The Effective Change Manager's Handbook: p 9-12, p186- p188, p223, p381



[Change Curve](#)

Phase 2: Solution Design

Key Activity

3. Define and Communicate the Governance, Roles and Change Responsibilities of Stakeholders

It is useful to think about the motives and interests of each stakeholder, as well as understanding the process of change for individuals or groups. This can help you to target and change your engagement and communications accordingly.

Segmenting helps a Change Manager to prioritise stakeholders and identify appropriate engagement, communication and influencing strategies.

Change Managers also need to determine who is key when working in a change team or with other stakeholders. Influencing third parties, defining the engagement roles in a RACI matrix, and assembling a written stakeholder strategy document are advisable.

This helps to co-ordinate everyone and proactively influence others so that they are aligned.



Engagement & Communications Strategy developed

Tools and techniques that can support this activity

RACI Matrix



Additional Information

Keep a running list of stakeholders. When working with a team, consider using a collaboration tool to share this list.



The stakeholder list then becomes a key document for stakeholder profiles and groups.

- APMG The Effective Change Manager's Handbook: P176, P199
- [RACI explained](#)

Phase 3: Development



Objective:
Plan the change



Outcome:
Support full business case development and creation of a formal plan (the roadmap) to achieve the change

Phase 3

Development

'Plan the change'

1. Engagement and Comms Plan developed

2. Change Management Plan developed

PHASE OUTPUTS	KEY ACTIVITIES			
<u>Engagement and Communications Plan developed</u>	1. Continue Stakeholder Mapping and Analysis	2. Finalise and Communicate the Governance, Roles and Change Responsibilities of Stakeholders	3. Finalise and Publish Engagement Plan	
<u>Change Management Plan developed</u>	1. Contribute to Draft Business Validation Plan (Aligned with Technical Testing Plan)	2. Refine Benefits / Disbenefits and Risk Assessment	3. Hold Future State workshops and finalise GAP Analysis	4. Finalise the Change Management Plan

Phase 3: Development

Engagement and Communications Plan developed

Introduction

Additional Information

- Overarching key messages to cover:
Why the change is necessary.
- What progress is being made with the plan in terms that are relevant to the people on the receiving end of the engagement activity.
 - Early examples of the desired change. The organisation is more likely to buy into the change if, for example, they see leaders embracing and displaying the desired change.
 - General related information, for example, what is being reported in the press, comments from the leadership team, or suggestions.

The Stakeholder Engagement and Communications Plan should have undergone development in the last two phases. In this phase we need to finalise and deliver our engagement plan to support the change adoption. Relevant messages should be communicated early and well. The aim is to keep people informed. Consistent communication using a variety of media channels, techniques, *and repetition*, is better than a one-size fits all approach – and you don’t need to have all the answers to communicate. To build trust with your stakeholder community, your engagement activities – including communications – need to be timely and within context.

Although FAQs (frequently asked questions) are often used in this type of planning, don’t get caught in the trap of believing that every question that has ever been asked should be included.

The key to successful FAQs is in the name ‘**Frequently** Asked Questions’. If you’re not careful, the question and answer list can become so long that nobody will ever read it, defeating the object from an engagement perspective.

Consider *what you are aiming to achieve* from each communication and the level of interaction that this will require, before deciding on the approach to use.

Key Activities

1. Continue Stakeholder Mapping and Analysis
2. Finalise and Communicate the Governance, Roles and Change Responsibilities of Stakeholders
3. Finalise and Publish Engagement and Comms Plan

APMG The Effective Change Manager’s Handbook: P248 - 250

[Explaining why organisational change is coming](#)


Phase 3: Development

Key Activity

1. Continue Stakeholder Mapping and Analysis

Stakeholder mapping and analysis does not just occur in the early phases but must be continued throughout. The commitment and capability of stakeholders can change so must be constantly reviewed.

Review the approaches and mechanisms of engagement, possibly broken down by particular segments or categories of stakeholder. This can help with prioritisation of those stakeholders to be engaged.




Ensure the stakeholder strategy contains how you will address the current and target gaps for stakeholders

Engagement and Communications Plan developed

Tools and techniques that can support this activity

Stakeholder Analysis Tool



Engagement & Comms Strategy




Comms Plan



Additional Information

Influencing strategies

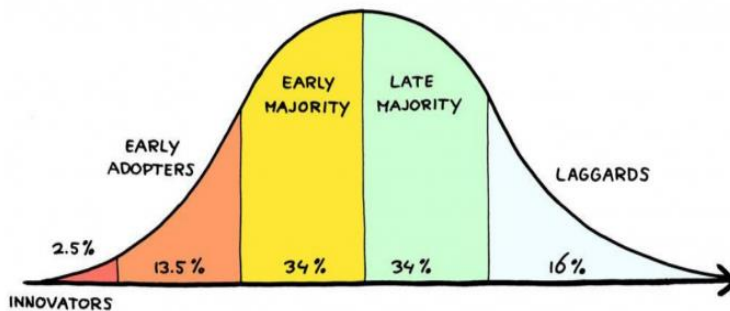

Everett Roger's innovation adoption model is relevant if there is a large population of stakeholders who all seem to have more or less the same power.

The strategy is to identify and target the early adopters and seek to recruit some of those opinion leaders to the role of Change Champion.

Also target and track the early majority, not allowing the change team to be distracted by the apparent apathy or resistance of the late majority.



APMG The Effective Change Managers Handbook, p.202-203 and p.298-299



[The adoption curve](#)

Phase 3: Development

Key Activity

2. Finalise and Communicate the Governance Roles and Change Responsibilities of Stakeholders

In **Phase 2** we used tools such as the RACI Matrix to define and communicate the governance roles and change responsibilities of stakeholders.

In this phase, we need to finalise this thinking, so that each stakeholder is clear on what their roles and responsibilities are during the implementation phase.

Think about what your governance structure and model will look like and how this fits in with the project and programme models.



Consider the change management roles and how they fit in with the programme governance framework e.g. Change Agent supporting the Programme Manager.

Engagement and Communications

Plan developed

Tools and techniques that can support this activity

RACI Matrix

	Chief Exec	Senior Responsible Officer	Medical Director	
Individual name, where known	Example Person	Example Person	Example Person	Example Person
1. Approve Budget	C	A	I	I
2. Approve Business Case	C	A	I	I
3. Approve Engagement Strategy	I	I	I	I
4. Approve Data Migration Strategy	I	I	I	I
5. Approve end stage boundaries	I	A	A	I
6. Approve PPD and associated documents	I	A	C	C
7. Create Change Network	N/A	N/A	N/A	N/A
8. Create draft future state processes	N/A	N/A	N/A	N/A
9. Agree with Clinical Reference Group	C	C	C	C
10. Business Continuity Plan	I	I	I	I
11. Review and approve plans	C	C	C	C
12. Review Go Live	I	C	I	I

Additional Information

Roles in organisation change include:

- Change Sponsors**
Individuals or groups with the power to determine that a change will occur
- Change Agents and Change Champions**
Individuals or groups responsible for seeing that a previously determined change occurs
- Change Targets**
Individuals or groups who are asked to change something (knowledge, skills or behavior) as a result of the change.



APMG The Effective Change Managers Handbook, Key roles in organizational change including team/project structures p.48 – p59.

[Who's in Charge of What?](#)

Phase 3: Development

Key Activity

3. Finalise and Publish Engagement and Comms Plan

The engagement and comms plan should have been completed to at least a high-level version in **Phase 2**

In **Phase 3** we need to finalise the plan, including all the relevant detail on how to implement the Engagement and Communications Strategy; who will deliver what, when, how and to whom.

Prepare key people for their critical influencer role. To set leaders and change agents up for success, change sponsors and communication teams collaborate to define their engagement role and ensure they are equipped with information, tools, training and support.

In this phase, we will begin preparing to deliver the early stage activities of the plan according to its schedule. One of the early activities we may need to prepare for will be the launch of the change initiative.



Engagement and Communications Plan developed


Tools and techniques that can support this activity

Engagement and Comms Plan



Additional Information

Always link what you measure to the engagement and comms strategy and key objectives and make sure that your plan includes the key activities you'll implement to support the change for all categories of stakeholders.



To support this, you might consider organising your engagement and comms strategy by target audience.

 APMG The Effective Change Managers Handbook, Key roles in organizational change including team/project structures p.48 – p59.

 [Example change programme launch event slides](#)

Phase 3: Development

Change Management Plan developed

Introduction



Additional Information

Executing a Change Management Plan is when...

- Change Networks and stakeholders are mobilised
- Toolkits are developed
- Implementation plans are deployed
- Transition plans are put together to ensure the organisation is ready to take on change.



In this phase, we are developing the ‘how’ and the detail of our change management solutions. These will address the people, process, structure and culture needs of the future organisation. They need to be ready to be executed in the implementation phase that follows this one.

The ‘how’ is contained within the Change Management Plan that needs to be finalised in this phase. This details how change is to be managed, executed and controlled.

We also need to plan how we will validate the business processes to ensure business requirements are met.

Stakeholder mapping and analysis should continue to be reviewed and governance, roles and change responsibilities of stakeholders finalised and communicated.

Key Activities

1. Contribute to Draft Business Validation plan (aligned with technical testing plan)

2. Refine Benefits / Disbenefits and Risk Assessment

3. Hold Future State workshops and Finalise GAP Analysis

4. Finalise the Change Management Plan

Remember ...

Just as a project has objectives to achieve, a change management plan has its own set of targets.

Change management plan objectives are:-

- to raise organisational awareness of the impending change and
- to help the affected teams adopt the change



APMG The Effective Change Manager’s Handbook: Developing a change management plan, p. 310



[Change Management Process](#)

Phase 3: Development

Key Activity

1. Contribute to Draft Business Validation Plan
(Aligned with Technical Testing Plan)

The Business Validation Plan will verify that the end-to-end business processes function as the requirements intended.

The plan should include:

- The **acceptance** criteria, against which to measure the business requirements
- The **resources** required for the business validation
- **Validation** activities (including duration) to test the business processes and any Standard Operating Procedures

The Business Validation Plan should be aligned with the Technical Testing Plan.



Change Management Plan developed

Tools and techniques that
can support this activity

Business Process Validation



Additional Information

The work should also look to provide a reconciliation between the anticipated benefits in the business case and what is expected following the testing work.




As part of the work, consideration should be given to ensuring any new offline processes are also considered in the testing!

Phase 3: Development

Key Activity

2. Refine Benefits/ Disbenefits and Risk Assessment

Benefits should now have been identified, quantified, valued, appraised and planned for. The next stage is about optimising benefits realisation by actively managing planned benefits through to their realisation; capturing and leveraging emergent benefits; and minimising and mitigating any dis-benefits.




Continue the assessment of risk ensuring any actions are planned for and implemented. If using a risk register, this should now be in place prior to implementation to formally monitor and update progress.

Ensure to plan for engagement activities related to change risks, such as status updates to project steering committees/senior leadership.

Change Management Plan developed

Tools and techniques that can support this activity

Benefits Realisation Plan



Additional Information

Planning for benefits realisation includes:

- Baselining performance
- Validating benefits with recipients/owners
- Prioritising benefits
- Identifying threats to benefits realisation
- Completing a benefits realisation plan (this acts as the baseline against which progress can be tracked)



APMG The Effective Change Manager's Handbook, Planning Benefits Realization p.155 to 163



[Benefits realisation](#)

Phase 3: Development

Key Activity

3. Hold Future State workshops and Finalise GAP Analysis

The GAP analysis that started in **Phase 1** (and was then developed further to a more detailed level in **Phase 2**) should now be finalised. Here we are building on that analysis work that looked at the current and future states and identified the change gaps.

To support this, future state workshops can be run, involving key stakeholders from across the business to design the future state processes based on the vision of the future that we began with. This could involve designing future state process maps.


By the end of this phase, we should know what the end outcome should look like and we can begin to document the ‘future state’ that will be finalised at the start of the next phase.

At the end of this phase we will also know the gaps that need to be addressed to reach the ‘future state’. This will allow us in the next phase to establish and deliver the plans needed to get us to there, via the Change Implementation Plan.

Utilise the Change Network, using the [Schein Model](#), to identify how the organisation culture is affecting the change.

Change Management Plan developed

Tools and techniques that can support this activity

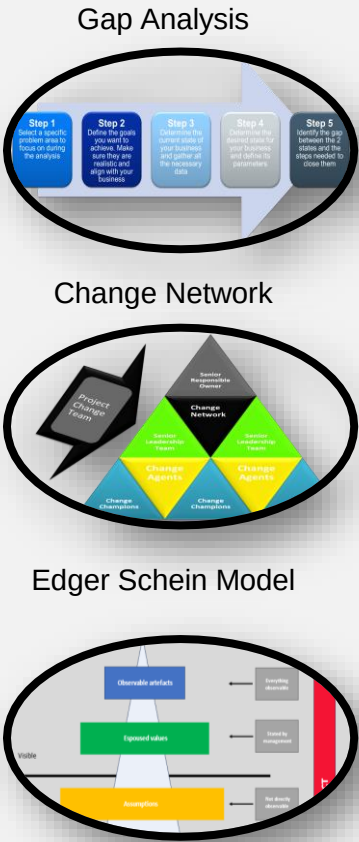

Additional Information

- Involve the Change Network in your Future State Workshops to:
- Discuss pain points within the current process and look at areas for improvement and ideate solutions.
 - Design the ideal future state experience (envision how you will deliver new value and a better experience to customers) and develop the future state process map.
 - Discuss those gaps that need to be addressed to achieve the future state.
 - An action from the workshop will be to document and sign off the ‘future state’, processes, finalise the gaps identified and develop the roadmap (Change Implementation Plan) that will deliver the future state.



APMG The Effective Change Manager’s Handbook, GAP Analysis p120-131, p262-264



[From journey maps to outcomes](#)

Phase 3: Development

Key Activity

4. Finalise the Change Management Plan

The Change Management Plan will have been ‘progressively elaborated’ throughout the project as new information became available or new levels of task detail were developed.

After the baseline plan, it will be continually refined, revised and updated to reflect current and expected progress.

Comparing a current or updated change management plan to an earlier version of itself helps us to *identify changes that may have a bearing on stakeholder expectations* and that may inform the project engagement and communications plan.

The Training Impact Assessment completed in


Phase 2

 should now be developed into a training plan that can be delivered in the next phase.

Change Management Plan developed


Tools and techniques that can support this activity

Change Management Plan



Additional Information

“Change management plans help you remain agile, adapt to challenges along the way, monitor success metrics and track milestones.” *Amy Kauffman, founder of Strategic Moxie*



Change management and planning, including engagement and communications, should begin as early as possible in the change process, to minimise the risk of the ‘grapevine’ filling in the gaps with rumours.



APMG The Effective Change Manager’s Handbook: Developing a change management plan, p. 310, Refine and update the plan, p.358



[Challenges of Grapevine Communication](#)


Phase 4: Deployment



Objective:
Manage implementation of the change



Outcome:
Establish/execute core plans for moving towards the future state

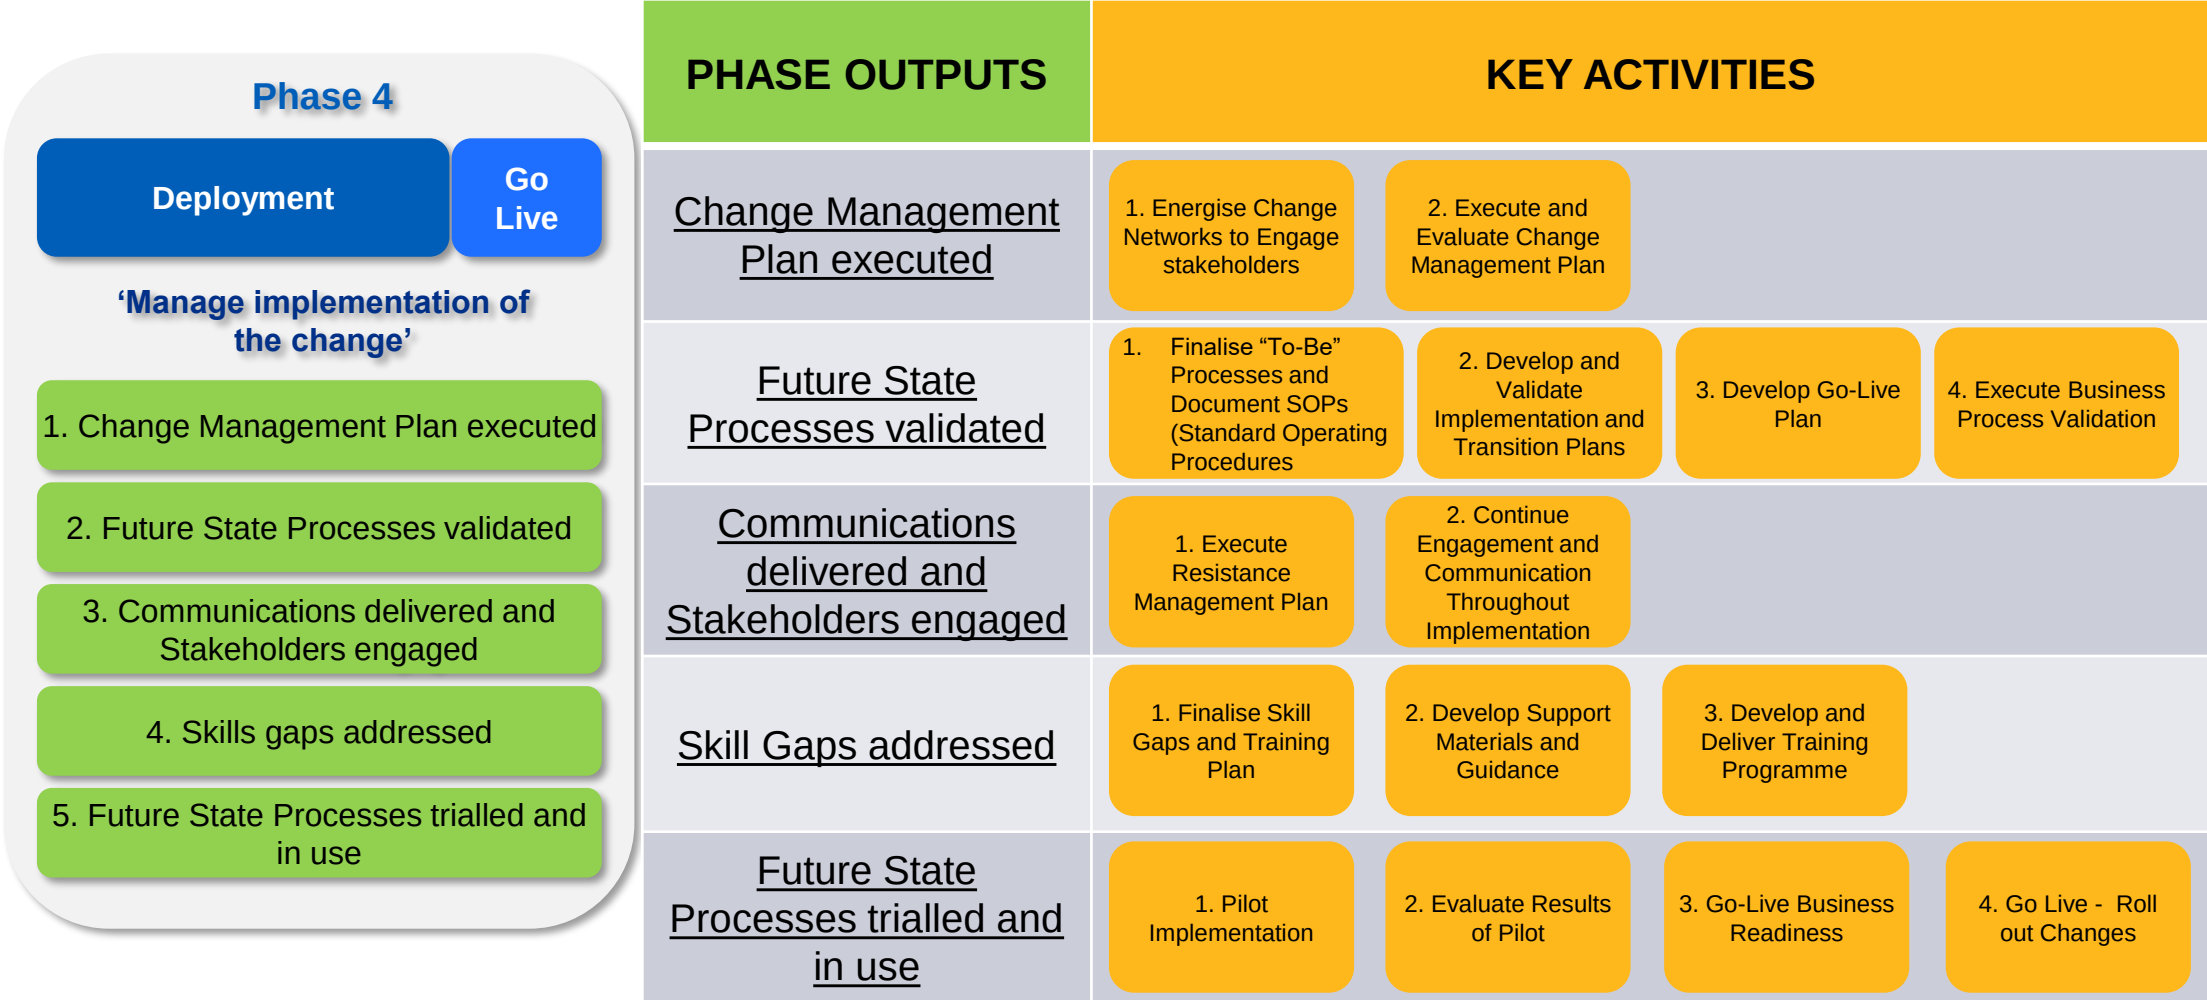

Phase 4: Deployment

Change Management Plan executed

The Change Management Plan defines activities and roles to manage the project baseline, ensuring that it is kept within project constraints.



A plan minimises any impact a change could potentially have on important stakeholders, staff members, the organisation or its customers.

Throughout change planning there will be a set of typical recurring actions that contribute to change readiness. A Change Management Plan is a good way to document these actions and ensure they are carried out.

Introduction

Given each organisation and every change is different, a 'one size fits all' Change Management Plan will not be successful. There are some key areas that will need to be covered in all plans:-

- **Stakeholders:** Who are they? Why are they important? How and when will you engage with them?
- **Engagement:** how engagement and communications are going to be targeted to different audiences?
- **Support:** how sponsors, the change team and change agents will be supported and developed to effectively manage the implementation and embedding of the change and what activities are planned to communicate the need for the change and increase buy-in?
- **Resistance:** what resistance can you expect and how will you deal with it?
- **Feedback:** how will stakeholders (including users) provide feedback on their thoughts and ideas about the change and implementation approach and how this will be fed into the change planning.
- **Measurement:** How you will know that your change interventions are working.

Key Activities

1. Energise Change Networks to Engage Stakeholders
2. Execute and Evaluate Change Management Plan



Additional Information

During the development of change management plans, it is important to consider concepts such as: effort versus duration, critical path, dependencies, milestones and best practice.

Change management plans must be integrated with other workstream plans.



They must be reviewed regularly to monitor progress against deliverables and the delivery timeline, and to consult on amendments or modifications to these plans.



APMG The Effective Change Manager's Handbook, p.310

[How to Make a Change Management Plan](#)


Phase 4: Deployment

Page 41

Key Activity

1. Energise Change Networks to Engage Stakeholders

The stakeholder mapping tool produced in previous phases informs the creation of appropriate and relevant Change Networks.

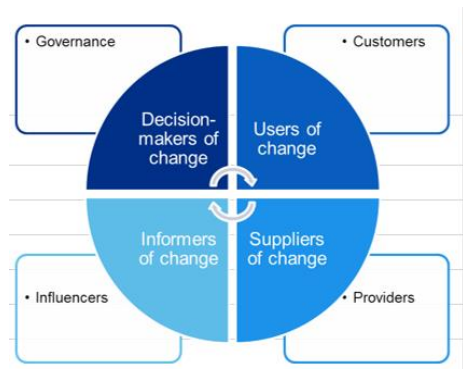


While Change Networks have been established in previous phases to engage **all** stakeholders, supplementing formal project related governance and operational hierarchies, this is the stage where they really come to life in supporting the change by:


- Assisting in deploying change management plans, as the networks not only understand the change but also can support its implementation most effectively;
- Acting as a two-way conduit of information between the project team and stakeholders impacted by the change.

Change Management Plan executed

Tools and techniques that can support this activity



Stakeholder Analysis Tool



Additional Information

There can be one or more Change Networks

Change Networks should be representative and inclusive of all stakeholder groups

Recognise the local organisational context when naming Change Networks

Ensure members of the Change Network are respected and trusted by their peers

Recognise the differences between change agents and change champions



APMG The Effective Change Manager's Handbook: Change Networks, p.294-297



[The role of networks in organizational change](#)

Phase 4: Deployment

Page 42

Key Activity

2. Execute and Evaluate Change Management Plan


The Change Management Plan records the set of activities that are undertaken and that enable the project to achieve adoption of the change. These activities typically include:

- Understanding local organisational context and the impact of the change
- Continuing to build awareness and support for the change
- Preparing the people in the organisation for the change required
- Identifying and proactively dealing with resistance to change
- It is important to measure the success of change activities at an organisation/department/function level (dependent on the size of the change) on an ongoing basis and to make adjustments as required. This can be managed through each individual implementation plan, that sits within the wider Change Management plan.

Change Management Plan executed

Tools and techniques that can support this activity

Change Implementation Plan



Additional Information

Think about how you will:-

- tailor the change management plan to the specific change and organisational context
- integrate the change management plan into the broader project plan
- measure the outcomes from the change plan and how they are to be presented to the project board – incorrect measurement of outcomes can lead to a false sense of achievement or failure
- keep measuring outcomes so that you can adapt where necessary



APMG Change Manager's Handbook: p 310 Developing a Change Management Plan and p 358 Refine and update the plan



[Metrics for Measuring Change Management](#)

Phase 4: Deployment

Future State Processes validated

Defines the future state process in diagrammatic and descriptive formats



Allows the development of Implementation Plans to move from current to future state.

Introduction

- The future state process map:
- Represents the goal of the improvement process in a diagrammatic form consisting of tasks and activities of the organisation’s transition from its current state to its future state.
 - Identifies how the process will be different in the future.
 - Provides the opportunity to capture inputs, outputs, steps and activities in a particular process and to identify improvements in cost, lead time, resource, quality and activity.

Key Activities

1. Finalise “To Be” Processes and Document SOPs
2. Develop and Validate the Transition Plan
3. Develop Go-Live Plan
4. Execute Business Process Validation



Additional Information

This should only be used when improvements to the process would change how the current process unfolds.

Before a future state process map is created, you should already have created a current state process map.

Don't rely on just visualisations of the future state. Textual descriptions to describe the new steps often identify gaps in the visual future state diagrams.



APMG The Effective Change Manager’s Handbook: p.564-575
Process mapping in MS Visio

Phase 4: Deployment

Key Activity

1. Finalise “To-Be” Processes and Document SOPs

The goal of your future state or “to-be” state map is to develop a process that eliminates obstacles you have identified in your current state map

The result: agreed work procedures that establish the best sequence of steps within each process

There are a selection of techniques that can be utilised to gather the required information, such as interviewing or brainstorming. Often delivered in a workshop format, you can use pre-printed sheets or flipcharts and Post-its or utilise an electronic or digital whiteboard. Online collaboration tools such as [Mural](#) can help.

The map can be represented in several ways e.g., block diagram, flowchart or swim lanes.

Involve the people who perform the “as-is” processes regularly because they will be best placed to support the generation of “to-be” processes.

Standard Operating Procedures (SOPs) are step-by-step guides that provide detail on the operations outlined in the process.


Future State Processes validated

Tools and techniques that can support this activity


Delivering Workshop Events



Process Mapping – As-Is and To-Be with examples



Aligning processes, procedures, validation scripts and training



Additional Information

Develop a phased approach to documenting processes and SOPs that maximises efficiency and ensures alignment with validation scripts and training.



Remember to include Business Continuity Management processes.



[As-is and To-be business processes](#)

Phase 4: Deployment

Key Activity

2. Develop and Validate the Implementation and Transition Plans

You should now know the future state, so the next step is identifying everything that needs to occur to implement the future state. This will form your Change Implementation plan which will include final delivery timeframes, milestones and key tasks to ensure a successful outcome.

Once a process has been improved, it's key that an initial baseline performance level is established. This should be continuously measured so that you can assess how well the improved process is meeting what was expected.


The transition plan will ensure there is a strategy in place that enables people to let go of the old ways, move into the neutral zone and progress to new beginnings. It's important to plan for after Go-Live and ensure adoption levels are monitored and activities are in place to support people transitioning to the 'new way'.

These plans needs to align to the expected project scope.


Future State Processes validated

Tools and techniques that can support this activity


Change Implementation Plan



Transition Plan



Aligning processes, procedures, validation scripts and training



Additional Information

Your **Implementation Plan** should **focus** on:

- Training needs
- Internal communication
- Customer communication
- Process and standard operating procedure (SOP) documentation
- Technology requirements, if needed
- Measurement systems
- Job description changes

Your **Transition Plan** should **focus** on:

- Criteria to assess adoption of the change
- Activities to ensure adoption of the change e.g. Quick wins (these may occur after Go-Live)



APMG Change Manager's Handbook: p165, p364, p481-486



[Implementation planning](#)

Phase 4: Deployment

Key Activity 3. Develop Go-Live Plan

The Go-Live Plan will include cutover activity, which sounds like ‘one event’ but is actually a series of tasks that are performed to **deploy** the components from the development/Pre-production environment to the Production environment and **activate** them, resulting in Go Live.




Once the Go-Live plan has been developed, the organisation can use it to assure stakeholders that all is ready to go live.

This activity to develop the Go-Live plan will be owned by the Project Manager for the duration of the project but the Change Manager will have an input on activities related to business change.

Future State Processes validated

Tools and techniques that can support this activity

Go-Live Plan




Additional Information

Ensure the plans contain a lot of detail about the **business change activities** leading up to the day Go-Live, the activities to be done on the day and then the activities to be done **after** the Go-Live is completed.

For example, you may need to reduce some services in the run up to a go live, to minimise disruption and there will then be post go-live activities to recover the service.

There will also be a ‘return to productivity curve’ for staff using a new system over time. This may affect services and will need to be planned to minimise its impact.

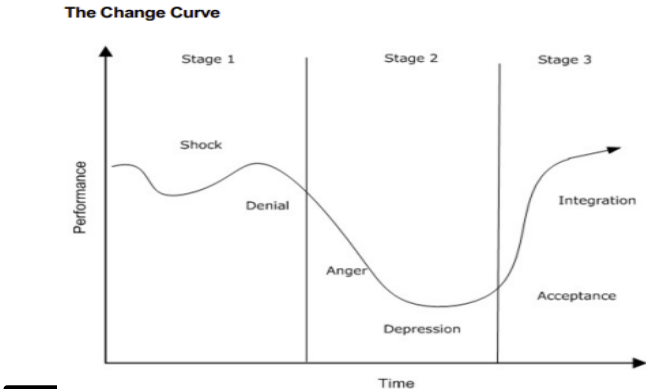

[Minimising a Productivity Dip](#)

Phase 4: Deployment

Key Activity

4. Execute Business Process Validation

Business Process Validation activities should be linked to the technical testing plans. Equal attention and testing should be given to each individual business process.

There should be full end-to-end business process testing to ensure that the business processes work with any existing business processes which haven't been changed as part of the transition.



Use functional test plans to ensure that all business activities are thoroughly tested and update functional test plans where business activities are missing. This could be a desktop exercise or could use a 'test' system where this is available.

Linking benefits back to the original business case is important in confirming the most likely outcomes following Go-Live.

Future State Processes validated

Tools and techniques that can support this activity

Business process validation script example



Additional Information

There should be testing of the downtime processes as well as the online processes.


There should also be a good understanding about what recovery processes look like in terms of keying data back into the system following downtime



Phase 4: Deployment

Communications delivered and Stakeholders engaged

When the real reason(s) for resistance to change are known, only then can progress be made to implement the change initiative.



Understand that change is *all about emotion* and will produce the same fight or flight instinct.

Introduction

Managing resistance is a vital as creating processes or any other element of implementation. Resistance can make or break a project.

With any kind of change, at work, or at home, resistance should always be expected – prepare for it! Preparation is key for any type of success and do not underestimate the amount of time needed for preparation.

There are different types of resistance. Knowing what they are will help in your resistance management plan.

Building and sustaining change momentum, while supporting managers and supervisors, is essential. Remember to take the staff on the same journey as you have set out for the change.

Timing of the momentum build-up is crucial: introducing change too early or too late will be detrimental.

A strong foundation for successful change is open and honest communication. Communications must be consistent in timing and in message.

Key Activities

1. Execute Resistance Management Plan
2. Continue Engagement and Communication Throughout Implementation



Additional Information

Expect resistance to change at a variety of difference levels and not always in the ways you might expect.

Some people resist openly whilst others will sabotage behind the scenes.

It's important to understand the reasons for resistance and tackle them and not the resistance itself.

Kotter and Schlesinger (2008) offer further help in building your resistance Strategy.

Overcoming Resistance to Change




Phase 4: Deployment

Key Activity

1. Execute Resistance Management Plan

Any change brings resistance, it's part of life. For any successful change project, resistance strategies should be built into the change plan. Unhappiness, disengagement, and sabotage can derail your change management project.

Managing stakeholders is key. [There are 10 common causes for resistance according to Kanter \(2012\)](#). Kanter also gives several ideas on how to deal with the reasons.




Creating a **Change Management Resistance Plan** will help to mitigate negative consequences of resistance.

Communications delivered and Stakeholders engaged

Tools and techniques that can support this activity


Resistance Management Plan



Additional Information

Resistance should always be expected – prepare for it!

Use the Change Network to develop a ‘Psychological Contract’



- Be honest about change, both benefits and dis-benefits
- Developing ‘media lines’ can be useful when rolling out potentially controversial functionality.
- Dig deep with resisting users to find out what they are really worried about.
-  APMG The Effective Change Manager’s Handbook: p 316 table 7.6 and p 317, p 314 for hints and tips on dealing with resistance
 -  [Change Resistance Management Plan Best Practices](#)
[Four Causes of Resistance to Change](#)

Phase 4: Deployment

Page 50

Key Activity

2. Continue Engagement and Communication throughout implementation

It's important to maintain a programme of engagement throughout a change initiative.

Building momentum for the change initiative takes a lot of effort and that's where a change network can help.

Communications and engagement with all stakeholders are part of building this momentum. Be reactive to the need to change the message frequency because high visibility of the change will keep the initiative high on people's priority list.



Different levels of engagement are required at different stages of the implementation.

Conduct workshops or informal discussions about the change programme with the impacted groups and across various levels of the organisation to gather information about who will most likely resist change and why.

Creating a **Change Management Resistance Plan** will help to mitigate negative consequences of resistance

Communications delivered and Stakeholders engaged

Tools and techniques that can support this activity

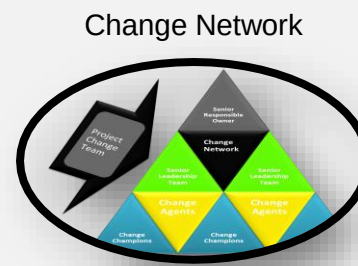

Additional Information

Change is all about emotion.

At all stages and in all engagement with stakeholders, be open and honest – tell it how it is, the good the bad and the ugly.

Explore multiple channels for communicating with all parties – it's a 2-way process.

Publish hard data updates and find good news stories to report to staff.

Find every opportunity to raise the profile of the change initiative.

[Nudge theory](#) can support you throughout your engagement and communications activity to ensure that you are encouraging people to make the choices that will best support the change initiative



APMG The Effective Change Manager's Handbook: p. 313 – 319





[How to communicate big change](#)

Phase 4: Deployment

Skill Gaps addressed	Introduction	 Additional Information
Support analysis of learning needs and identify skills gaps.  - Collaborate on development of learning and development plans. - Contribute to implementing the plans and evaluate the effectiveness of the learning.	Any type of change programme is likely to involve a skills gap that needs to be filled. As a Change Manager, you will rely heavily on expertise in other areas, and training is one of them. It is essential to support, collaborate and contribute to their work because the change gap and skills gap are inter-dependent. For example, as part of an integrated approach to engagement and skills, Ways of Working (WoW) events can bridge the gap between the two by answering the ‘Why are we doing this?’, ‘What’s all this about?’ and ‘How will it affect me?’ questions before the formal learning sessions. This maximises the time for learning ‘how’ to work in the new world. Key Activities 1. Finalise Skills Gaps and Training Plan 2. Develop Support Materials and Guidance 3. Develop and Deliver Training Programme	Comms and Training should blend seamlessly from high-level ‘why’ to detailed ‘how’ messages.  Branding and messages need to be consistent throughout. Ways of Working (WoW) can help people to understand how their work is going to change, providing both engagement and priming for future learning.  APMG The Effective Change Manager’s Handbook: p.367- 414  Education and Training Standards - NHS England

Phase 4: Deployment

Key Activity 1. Finalise Skills Gaps and Training Plan	Skill Gaps addressed	 Additional Information
During the change impact assessment we consider the complexity of the new process and how similar it is to their current process. This now provides input into a skills gap analysis. The skills gap analysis (AKA learning needs analysis or training needs analysis) produced during Phase 2 should now be finalised in preparation for development and delivery of training or other learning intervention, where appropriate. The training impact assessment produced during Phase 2 can now be developed into a training plan, providing a clear description of the intended training solution and how that training solution will be implemented. It will provide the detail about how, when, where and with whom each stage of the training solution will be undertaken, and who is responsible for ensuring that it happens.	Tools and techniques that can support this activity 	A training plan answers the questions:- - What will be delivered to meet the skills gap ? - How will it be delivered? - When will it be delivered? - How will we know it's been successful?   APMG The Effective Change Manager's Handbook: p385-394  Learning Needs Analysis and Training Planning

Phase 4: Deployment

Key Activity

2. Develop Support Materials and Guidance

As the training team begin to develop materials to support the skills gap, they will be looking to the Change Manager to inform this development.




Future state processes provide the input into Ways of Working (WoW) workshops designed to ensure that operational processes are clearly understood before ‘how to’ training is delivered. WoW support materials are developed by the change team with support from the training team.

Standard Operating Procedures (SOPs) provide the input into ‘how to’ training and support content. Training support materials are developed by the training team with support from the change team.


Skill Gaps addressed

Tools and techniques that can support this activity

Aligning processes, procedures, validation scripts and training



Developing and Delivering WoW Events



Additional Information

- Remember to develop materials with Adult learning principles in mind.
- Malcolm Knowles (1970) suggested in his work on Andragogy that Adults:-
- Are self-directed
 - Come to training with a lifetime of existing knowledge, experience, and opinions
 - Are goal-oriented
 - Want training that is relevant
 - Want training that is task-oriented
 - Learn when they see “what’s in it for them”
 - Want to be and feel respected



[Principles for Adult Learning](#)

Phase 4: Deployment

Key Activity

3. Develop and Deliver Training Programme

- It's important that the training team:
- Develops a schedule for learning activities, taking into account estimated learning time and the number of staff requiring each module.
 - Develops a delivery approach that meets the needs of the organisation, e.g. face to face training, self-directed online learning, supported virtual learning or curated content only.
 - Considers relevant learning styles and methods.
 - Makes sure the learning objectives are clear and in line with the goals of the change programme and the wider organisation and that evidence measures are in place.

Delivery can begin as soon as is relevant for the programme.


Skill Gaps addressed

Tools and techniques that can support this activity

Design a Training Programme



Linking training to business objectives



Additional Information

Ideally, learning activities should be delivered ‘just in time’, immediately before the change is implemented and learning will be used.



Where this is not possible, refresher activities such as regular comms and support will be required.

It is important that Change Managers work in close partnership with Training colleagues to achieve the best outcomes.



APMG The Effective Change Manager’s Handbook: p. 391-394



[Learning in the Flow of Work](#)


Phase 4: Deployment

Future State Processes trialled and in use

Introduction

Additional Information

The purpose of deployment is to move new or changed processes (or any other component) to live environments. It may involve pilots, testing and evaluations.



There are a number of distinct approaches that can be used for deployment.



The change elements of what the Project team will probably refer to as the ‘Cutover Plan’ should be owned by the Change Sponsor for the change initiative. In reality, it’s more than a cutover from one system to another and should be viewed as a ‘Transition’ from the old world to the new one. It should provide assurance that the organisation, people and processes are in an agreed state of readiness for Go-Live.

Transition activities, and the level of input to the cutover plan, should be based on the complexity of the change initiative. This should not be used in isolation but should be reviewed and updated throughout the implementation process. The cutover document should be used in conjunction with the Go-Live Readiness Checklist and the Business Readiness Checklist

Key Activities

1. Pilot Implementation
2. Evaluate Results of Pilot
3. Go-Live Business Readiness
4. Go-Live - Roll out Changes

Cutover and transition planning is not a last minute tick job. The Change Manager should collate evidence that supports a smooth transition throughout the implementation process.



Specific activities will require owners. Make certain that each person is aware of their individual responsibility and the deadlines through a RACI.



APMG The Effective Change Managers Handbook, Rollout approaches p.359 – 361



[Roadmap to a Successful Large-Scale Tech Cutover](#)

Phase 4: Deployment

Key Activity 1. Pilot Implementation

Piloting an upgrade or change provides assurance to stakeholders of the following:

- A plan to implement a structured validation of changes. Pilots also support a test process that provides fact-based evidence (that services match agreed requirements and deliverables).



- Quality assurance of service components and service capability of a change or upgrade.
- Identifies, assesses and addresses issues, errors and risks prior to full roll-out of a new service or change.
- Provides confidence that the change/new initiative will deliver the desired outcome and benefits to the stakeholder.

Future State Processes trialled and in use

Tools and techniques that can support this activity

Pilot plan



Additional Information

Define stakeholders, set goals and plan the timeline.
Ensure senior level buy-in and involvement of a relevant 'user' stakeholders, including clinicians.
Select varied participants to ensure a wide range of use-cases/scenarios are proven.
Have a clear plan and define a feedback loop.



Define clear communications and set expectations
Establish regular meetings to assess progress.
Have a period of validation after the pilot has gone live to establish success of pilot.



[Running a Successful Pilot Project](#)

Phase 4: Deployment

Key Activity


2. Evaluate Results of Pilot

It's important that you think about what the pilot has taught you and how it might influence wider rollout recommendations, as necessary. This is often achieved through a 'lessons learnt' activity that is likely to be run at a project level but it's important that change management lessons are included.

- Key Performance Indicators (KPIs), Service Level Agreements (SLAs) and benefits are useful tools that enable the evaluation of results after a pilot.
- The type of services that will be implemented may vary from basic to highly complex, therefore the use of KPIs, SLAs and benefits is likely to vary depending on the type of change.
- KPIs for each service should therefore be agreed with the Change Sponsor, the supplier and customer representatives as soon as the MOU has been agreed.
- Service Level Agreements outline how a service will be supported and buy-in from the supplier is crucial, as they will more than likely provide technical support.

Future State Processes trialled and in use

Tools and techniques that can support this activity

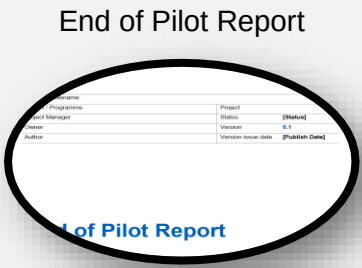

Additional Information

Think about KPIs that will demonstrate how well the new initiative is performing.

Do not create KPIs at random. Get buy-in from the customer and supplier.



Use KPIs in conjunction with agreed benefits and SLAs, as this will enable a holistic view of expected outcomes matched against the actual performance.

Phase 4: Deployment

Key Activity

3. Go Live Business Readiness

Before a new change/upgrade has gone live, it is important to measure the business readiness to adopt the change.

In earlier phases, a Change Management Plan was developed based on an impact assessment (to measure the complexity of change and the effort required to manage it).




Plans were also made to transition to the future state and, at the same time, plans for technical cutover will have been made. It is important now to check that the business is ready to adopt the change, with people and process readiness included in your readiness assessment criteria that can then be used as input for the cutover/go live plan.

The Business Readiness Assessment will vary depending on the complexity of the change, whether it is being delivered as a ‘big bang’ deployment or multiple rollouts.

Future State Processes trialled and in use

Tools and techniques that can support this activity

Go-Live Business Readiness Assessment



 Additional Information

When identifying criteria for your Business Readiness Assessment, consider:

- People readiness
- User support
- Comms
- Skills development
- Process readiness
- Familiarity with SOPs
- Understanding of workarounds

Any document should be used as a framework rather than a hard-and-fast set of activities that need to be applied to every change initiative.

It is important that the Change Manager demonstrates that they have continuously assessed an organisation is ready to transition into an agreed changed state.

Phase 4: Deployment

Key Activity
4. Go-Live – roll out changes

The Go-Live Checklist is a tool owned by the Project Manager for the whole project but should include business readiness that is the Change Manager’s input. The Change Manager can use this checklist as assurance of the expected and actual service deliverables and any integrated elements that each change or new initiative depends on to transition into the live state. These elements include Customer Readiness, Testing, Go-Live Readiness and Implementation Verification.

The Checklist is a high-level document and should not be confused with Customer Business Readiness or the cutover documents, as these documents are more detailed and specify tasks roles and responsibilities.

Check the Go Live Checklist one last time – hold a brief all staff meeting to run through final readiness checklists and respond to last minute questions. This may be run by the project manager but the Change Manager can update on business change elements.


A Go-No Go Decision will be made. If agreed to go live then it's time to pull the switch. If the decision is to not go live, then any issues will need to be addressed and then another call arranged to assess readiness to go live.

Be sure to take time to acknowledge all you have learned and done. Create short-term wins and celebrate your success.

Future State Processes trialled and in use

Tools and techniques that can support this activity

Go-Live Business Readiness Assessment



Create Short-term Wins



Additional Information

Look at each change individually and assess the required readiness elements.

.



Use the Go-Live checklist throughout the implementation and update accordingly.



APMG The Effective Change Managers Handbook, Deployment Checklist p.361
[Generating short-term wins](#)

Phase 5: Post Deployment



Objective:
To measure adoption, identify gaps and reinforce the change



Outcome:
Change is embedded and sustained

Phase 5

Post Deployment

'Reinforce and sustain the change'

1. Change adoption evaluated

2. Business Change refinements actioned

3. Change sustained

PHASE OUTPUTS	KEY ACTIVITIES			
<u>Change adoption evaluated</u>	1. Collect and Analyse Data	2. Collect and Analyse Feedback	3. Hold Post-Implementation Review (PIR)	4. Diagnose Gaps
<u>Business Change Refinements actioned</u>	1. Plan Corrective Actions	2. Deliver Plan		
<u>Change Sustained</u>	1. Continue Data Collection and Analysis	2. Celebrate Successes		

Phase 5: Post Deployment

Change adoption evaluated

Once a change has been implemented it is important to make sure the goal of what you set out to do was actually achieved.

This includes not just measuring the benefits but seeing if further improvements can deliver still greater benefit through the process of “optimisation and continuous improvement”.



The people impacted by the change (internal and external) provide valuable feedback to assess how well the change has been accepted and utilised and help to identify areas where there is still work to be done!



Introduction

There is the tendency to believe the change is finished once it has been implemented but it is important to assess the impact of the change post deployment.

The success of any change is at its highest risk of failure at the point of adoption. This is because it is new and fragile, full of uncertainties and unknowns. It is in limbo between the people who built it - and the people who will own it - so there is a lot of work for the Change Manager to do alongside impacted teams to put strategies in place post implementation to make the change stick and stay stuck!

Key Activities

1. Collect and Analyse Data
2. Collect and Analyse Feedback
3. Hold Post-Implementation Review (PIR)
4. Diagnose Gaps



Additional Information

Whilst Post Deployment is the final part of the change process, the activities required to sustain change start right at the beginning of the change journey – at the point when it just an idea! The Change Manager should also look to incorporate activities and criteria to reinforce and sustain the change in the solution design and planning stages. The transition plan should include efforts to sustain the change.



Change Management continues way past implementation by ensuring the benefits are delivered, the change sticks and that it stays stuck.



APMG The Effective Change Manager’s Handbook: Sustaining Change, p.454 – 491



[Model for Sustainable Change](#)

Phase 5: Post Deployment

Page 62

Key Activity

1. Collect and Analyse Data

During the post-deployment stage, data needs to be collected to review how effectively the change has been introduced and adopted and where further work is needed to make the change stick.

Earlier in the Toolkit, several tools were described that support these activities and these tools (detailed below) can now be revisited to measure successes and failures and to plan corrective actions.



Another useful tool at this stage is the “Sustainability Risk Assessment” which highlights the top three risks or issues that will prevent the change from sticking or staying stuck, and therefore prevent return on investment and benefits realisation.

This is where the benefits will be revisited. Is there further work to be done to realise the benefits?

Use the [Schein Model](#) to look at whether the culture within the organisation has had an impact in embedding the change.


Change adoption evaluated

Tools and techniques that can support this activity


Benefits Realisation Plan



Tipping Point and Critical Mass



Leverage



Vicious and Virtuous Cycles



Sustainability Risk Assessment



Edger Schein Model



Additional Information

The data you collect needs to answer the following questions:

- How do we know the new ways are working?
- How do we know the old ways have stopped?
- How will we know performance has improved?
- How will we know when the change has reached its tipping point and critical mass?
- When will we know the change is fully complete?
- How will we learn lessons from implementing the change?
- How will we learn lessons from adopting the change?



APMG The Effective Change Manager's Handbook: Levers p460-471, Tipping point p474-475, Vicious & Virtuous cycles p476-480, Benefits Realisation p160-162, Sustainability Risk Assessment p488-489



[Critical Mass and Tipping Point in Change Efforts](#)

Phase 5: Post Deployment

Key Activity

2. Collect and Analyse Feedback

Stakeholders will have many different views of how the change impacts them and is not enough to assume that the change has been a success because it has been deployed.

At this stage, it is necessary to use mechanisms to capture feedback from those affected by the change to ensure any issues or areas of resistance are uncovered and corrective actions agreed.



Stakeholders are more likely to accept change if their opinions are valued. Gathering feedback, therefore, encourages a culture that embraces change rather than feeling that “change is done to them”.

A strong sponsor network can be created by mapping out a [change network](#). This network involves people from across the organisation, made up of Change Champions and Change Agents.

Change adoption evaluated

Tools and techniques that can support this activity



Additional Information

However you choose to gather feedback, information gathered should indicate:

- whether the change has been accepted by the recipients or whether there is still work to do to embed it
- levels of confidence in the benefits of the change
- areas of resistance to the change
- issues or problems affecting adoption
- performance levels and any reductions in performance as a result of the change
- attitudes to the success of the change and whether further improvements are required



APMG The Effective Change Manager's Handbook: Measuring change effectiveness and methods of capturing information and feedback p320-327



[How to Analyse Survey Data: Methods and Examples](#)

Phase 5: Post Deployment

Key Activity

3. Hold Post-implementation Review

It is recommended to carry out an initial Post-implementation Review (PIR) when the change is still fresh in people’s minds, when issues have started to be ironed out and observations noted. It’s recommended to conduct a full Post Implementation Review (PIR) at a later stage, when the changes start to truly take effect.




Often the Post-implementation Review is missed as priorities move to the next project. However the PIR is a valuable tool to assess how well or, in contrast, how badly the change went. Conducting a PIR can help with lessons learnt for future change projects and in turn encourage a culture of continuous improvement.

Change adoption evaluated

Tools and techniques that can support this activity

Post Implementation Review (PIR)



Lessons learnt

What went well	What didn't go well	Other learnings
✓ support from project management during client negotiations could be better	✗	?
project manager is a great motivator		
accounting should have been involved earlier		
lack of experience in oil and gas industry		
		great team work



Additional Information

A useful approach to measuring whether the change was a success and to encourage continuous improvement is to carry out a “Post-implementation Review (PIR)”



The PIR answers the questions:

- 1. Did the project fully solve the problem that it was designed to address?
- 2. Can we take things further, and deliver even bigger benefits?
- 3. What lessons did we learn that we can apply to future projects?



[Post-Implementation Reviews - Project Management from MindTools.com](#)

Phase 5: Post Deployment

Page 65

Key Activity 4. Diagnose Gaps

Towards the end of the change there is the tendency to be overconfident in what has been achieved, so it's important to identify any gaps or issues. An adoption checklist may be useful to ensure the right questions are asked to analyse how well the change has been adopted and to identify interventions needed to close any gaps.

At this point the "Transition plan" should be revisited to ensure individuals and groups are supported throughout their transition. People transition at different paces; just because one area has fully embraced the change doesn't mean that others have.

Revisit the Change Management Plan to diagnose gaps. It should have measurements that will show whether the change has been a success. Were the change management activities in the plan effective? It's important to look for early warning signs that could prevent the benefits being realised, particularly in the longer-term.


Change adoption evaluated

Tools and techniques that can support this activity


Adoption Checklist



Transition plan



Change Management Plan



Additional Information

There are many things that can impact adoption and support for the change, some foreseeable and some not.



Typical "barriers" or gaps requiring monitoring and corrective action are:

- Too much change or "change fatigue"
- Recipients are not ready
- Disruptive behaviour or "derailing the change"
- Lack of positive or negative consequences for changing
- Inaccurate measurement
- Unwillingness to realise the benefits
- Lack of resources or money
- Human behaviour - "humans will be humans" and can be an unstoppable force



APMG The Effective Change Manager's Handbook: p 364, 481 – 483



[Leading change & transition](#)

Phase 5: Post Deployment

Business Change Refinements actioned

It is important to remember that diagnosing gaps and implementing corrective actions is an ongoing activity, performed at several stages of the change project and not just in the reinforcing change stage.



Finding the root cause of a problem can be challenging but once the cause is established, it is important to agree the actions needed to address it.

Introduction

Humans love the status quo and will go to great lengths to sustain it. Often, people turn a blind eye to change initiatives long before it's possible to realise the benefits and see them in action.

The feedback you gather in this phase will indicate whether any issues persist, for instance resistance to the change or lack of adoption. It's important to keep monitoring these issues until actions are in place to resolve them by looking at root cause.

As well as agreeing the actions needed, it is important to plan how and when they will be delivered. A Post-deployment Plan can help to ensure ownership and completion of corrective actions, in turn maximising the chance of the change being a success.

Key Activities

1. Plan Corrective Actions
2. Deliver Plan



Additional Information

It is the Change Manager's role to identify dependencies across different stages of the change. For example, making sure a change has stuck before moving onto the next phase. This is a continuous activity and not something which is only done after implementation.



APMG The Effective Change Manager's Handbook: P350- 358



[Root Cause Analysis](#)

Phase 5: Post Deployment

Page 67

Key Activity

1. Plan Corrective Actions

It is important at this stage of the project to look for ways to close the gaps or issues, which have been revealed from the data and feedback collected earlier.

- Analysis of the root cause of issues or gaps – and the development of plans to address these – will enable corrective actions to be put in place.



- [Nudge Theory](#) is based upon the idea that by shaping the environment, also known as the choice architecture, one can influence the likelihood that one option is chosen over another by individuals. A key factor of Nudge Theory is the ability for an individual to maintain freedom of choice and to feel in control of the decisions they make.
- The [Schein model](#) can be used to discover if the culture within the organisation means the change has not been realised.

Business Change Refinements actioned

Tools and techniques that can support this activity

ADKAR model



Nudge Theory



Edger Schein Model



Additional Information

The ADKAR model is a useful model to determine whether the root cause of a problem area was due to lack of awareness, desire, knowledge, ability or reinforcement.



This could be, for example, providing further communication to a particular audience, applying incentives to increase motivation, providing training to upskill staff, redesigning processes, ensuring on-the-job assistance is in place, reporting on performance and so on



APMG The Effective Change Manager's Handbook: p 362, 487




[ADKAR model](#)

Phase 5: Post Deployment

Key Activity 2. Deliver Plan

Once the corrective actions have been identified they need to be delivered.

Quite often, at this stage of the change priorities have already shifted to the next project. It's important, therefore, that the corrective actions in the Change Management Plan are given priority.




Deliver cut-down versions of the Change Management Plan, Implementation Plan (align with any technical aspects) and Transition Plan that will address the corrective actions.


Business Change Refinements actioned

Tools and techniques that can support this activity


Change Management Plan



Change Implementation Plan



Transition Plan



Additional Information

Planning for a change *which will be sustained* requires:

- Consideration of budget, resource and focus until the change is sustainably delivered.
- Analysis of the criteria and targets until the change is sustainably delivered.
- Governance to be in place until benefits have been realised
- Re-visiting the benefits to ensure benefits realisation and re-alignment if needed.
- Re-visiting the risks to ensure risks are still being captured and mitigation strategies developed.



APMG The Effective Change Manager's Handbook: P358



[Corrective Action Explained](#)

Phase 5: Post Deployment

Change Sustained	Introduction	 Additional Information
For change to stick, activities must be put in place to sustain it. Otherwise, there is the risk that people will go back to their old ways or “status quo”, as this is a comfortable place to be. When stakeholders are motivated to change, risks and rewards are understood. When the change is embraced as beneficial to the organisation and to each stakeholder, then it has a much higher chance of being sustained. .	There are many reports of change initiatives failing or falling short of fulfilling their change vision. One well-known example being Apple’s Lisa computer that failed to engage consumers as predicted, in spite of its vast development resource and technical advances. Prosci cites three factors for successful and sustaining change: ▪ Strong leadership from leaders, who know the value of continuing change management activities post deployment and who communicate that the work is not over yet ▪ Measuring adoption and putting the work in to understand the value of the data collected ▪ Communication that encourages feedback, which means – if possible – encouraging participation to make people feel heard and supported	Managers and leaders have one of the biggest influences on a person’s decision to adopt and sustain change. Research has shown that people are more likely to adopt a change if their direct manager discusses it with them, rather than a senior leader or a representative from another area.  Our tendency to listen to the boss and the wish to please the boss has an impact on our acceptance of change.  APMG The Effective Change Manager’s Handbook: Sustaining Change, p.454 - 491  Sustainable change
	Key Activities 1. Continue Data Collection and Analysis 2. Celebrate Successes	

Phase 5: Post Deployment

Page 70

Key Activity

1. Continue Data Collection and Analysis

Data collection and analysis should continue to ensure the intended benefits are still being achieved and the change is being sustained.

Continuous reporting is important to provide evidence that the intended outcomes are still being achieved.

Ongoing analysis is needed to spot possible changes in direction or in approach, which are required to ensure the greatest chances of success.

You can use the Edger Schein Model to understand possible changes in direction or approach

- Focus on the specific problem
- Engage a group to find out what is causing the problem
- Create the right environment
- Specify the change goal
- Build a change program to rectify



The period of data collection will depend on whether the longer-term benefits have been realised or not.


Change Sustained

Tools and techniques that can support this activity

Benefits Realisation Plan



Edger Schein Model



Additional Information

Remaining vigilant to what is happening over the broader landscape will help to ensure the change is sustained.

Continuous data collection and analysis can help to reveal:

- If the planned activities are still the right ones.
- If the data being collected is highlighting benefits, lessons learnt and generating ideas for improvement.
- If a change of direction is needed as a result of new information or changed circumstances.



APMG The Effective Change Manager's Handbook: P155-156



[Cost-Benefit Analysis of Change Management](#)

Phase 5: Post Deployment

Page 71

Key Activity 2. Celebrate Successes

Early adoption, success and long-term wins must be recognised and celebrated.

Recognition is needed in order to cement or reinforce the change.

Early successes, however small, provide evidence of the benefits that the change is bringing.



Celebrating successes increases moral and builds support and buy-in from people who may need to "see it to believe it".

Change Sustained

Tools and techniques that can support this activity

Engagement and Comms Plan



Celebrate Successes Activities



Additional Information

For change to stick, successes (however small) need to be celebrated.

Some examples of ways to celebrate success are:

- Recognition of achievement.
- Regular communications of success.
- Recognising where new behaviours are in place.



APMG The Effective Change Manager's Handbook: p 481 - 483




[Reinforcing change through celebrating success](#)

Appendices


- [Plans within Change Management and how they fit together](#)
- [Change Management Maturity Self-Assessment](#)

A structured self-assessment based on 12 change management toolkit components/themes. Provides gap analysis and guidance for advancement through maturity levels. Linked to change management tools and techniques.

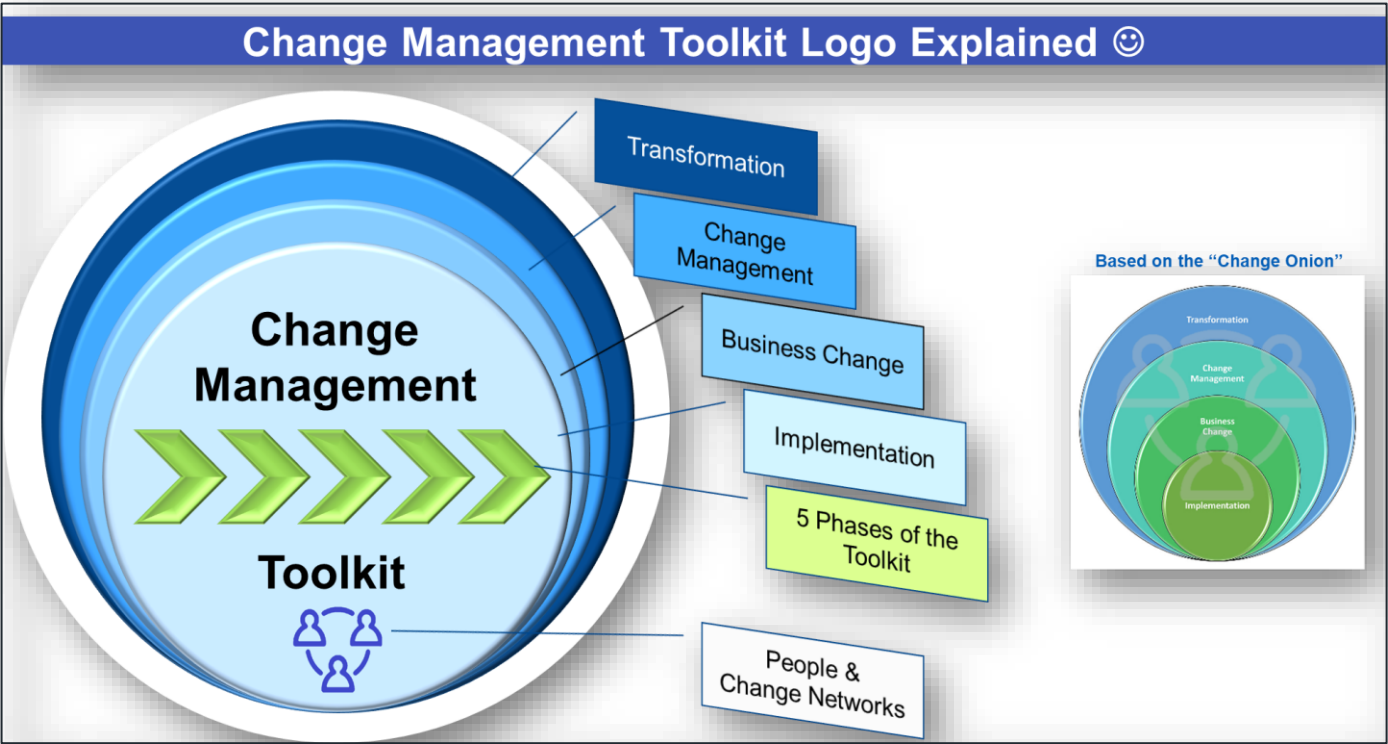

Plans within Change management

Once the change has been defined and the solution designed, we need to put together ‘how’ we will achieve change through a series of plans that start by looking at the bigger picture with the ‘Change Management Plan’ and then drilling down into the detail and defined steps that will achieve the desired outcome.

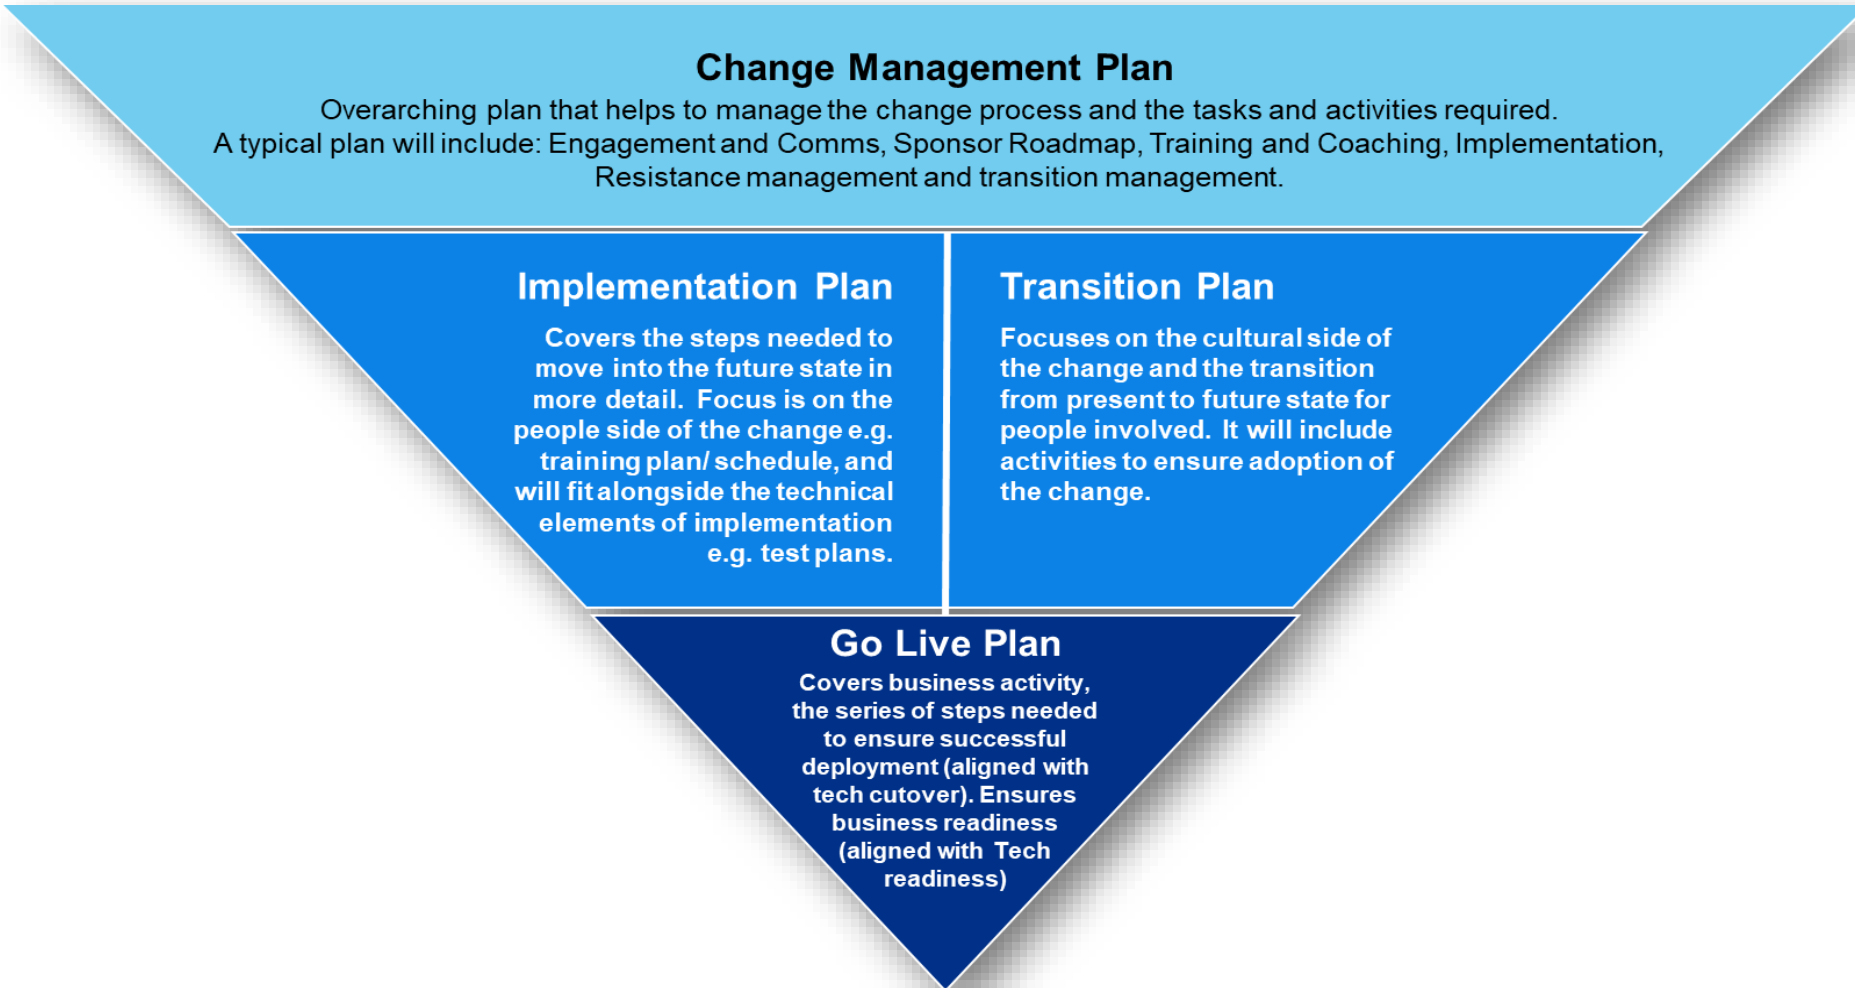

New to Change Management?

Hello and welcome

This Toolkit is a resource for anyone involved in managing change, whether as a Programme, Project or Business Change Manager. The Toolkit details a framework for change with typical phases and associated tasks and activities of a change project, including the people side of change.

Change management explained using the Change Onion!

Starting with the core, there's Implementation - straightforward implementation, usually of tech, that does not impact on any business processes (**or does it?**).


Then there's Business Change - the process of moving from current to future state processes, often led by people who know the process well but they can sometimes pay more attention to the process itself than the people who work with the process.

That's where Change Management comes in - this is the 'art' of bringing people on the journey that is moving from current to future state. Often overlooked, a great tech solution with clearly mapped processes and procedures will not deliver benefit unless the people are bought in to and working happily in the 'new world'.

Where all of these layers are added, one onto the other, the utopia of business transformation can occur.

That can be a problem when organisations have a team working on an implementation, another one looking at business change and a different team looking at change management - if they're lucky. This can only lead to disjointed working and disruptive change is the inevitable result, so binding these layers is the challenge facing most organisations as they strive for business transformation

The Change Onion



[Click here to start exploring the Change Phases](#)

[Click here to access the Change Management Group](#)




Join the Change Management Network

The Health and Care Change Management Network

NHS England Transformation Directorate's Health and Care Change Management Network is a collaborative space for those interested in change management or undertaking change initiatives of any size or complexity, especially but not exclusively related to Digital, Data and Technology (DDaT).

The Change Management Network can help you by giving you access to the Change Management Toolkit and over a hundred tools, including the [Change Management Maturity Self-Assessment](#), the Discussion Forum or the Learning and Support materials.





Change Manager

Hello and welcome

This [Toolkit](#) is a resource for anyone involved in managing change, whether as a Programme, Project or Business Change Manager. The Toolkit details a framework for change with typical phases and associated tasks and activities of a change project, including the people side of change.

As a change manager, you encounter many challenges while leading and implementing change within an organisation.

The Change Management Toolkit presents a Change Management Framework that gives you access to many different tools, techniques and approaches to support you in your change initiative.

The toolkit can help you:

- Implement changes that positively impact the organisation, its **people** and its **efficiency** in supporting better **patient outcomes** and **satisfaction**.
- Communicate the benefits of Change Management across the organisation, making it **easier**, more **cost effective** to navigate transitions successfully and create a more **transparent and informed work environment**.
- Proactively manage resistance and increase the chances of successful implementation.
- Incorporate change management practices into routine activities, to encourage **innovation and adaptability**.

[Click here to start exploring the Change Phases](#)

The Change Management Toolkit [Framework](#) provides a **roadmap** for managing complex projects, allowing Change Managers to leverage proven strategies and best practices to **achieve desired outcomes**.



The Change Management Toolkit provides Change Managers with resources to **plan, execute, and monitor** change initiatives effectively.



Join the Change Management Network

The Health and Care Change Management Network
NHS England Transformation Directorate's Health and Care Change Management Network is a collaborative space for those interested in change management or undertaking change initiatives of any size or complexity, especially but not exclusively related to Digital, Data and Technology (DDaT).

[Click here to access the Change management Group](#)

The Change Management Network can help you:

- Get access to the [Change Management Toolkit](#) and all the latest updates.
- Access over a hundred tools and useful links to help with all phases of Change Management.
- Get access to the [Change Management Maturity Self-Assessment tool](#)
- Interact with the [Discussion Forum](#) to ask questions, seek advice and keep up to date with the latest Change Management developments.

Project Manager

Change management (and change managers) provide essential assistance to project managers through:

- **Handling Resistance:** Helping project managers navigate potential roadblocks and maintain project momentum through identifying and addressing resistance using effective communication, stakeholder engagement, and mitigation strategies.
- **Engaging Stakeholders:** Identifying key individuals and groups affected by the project and working closely with them to understand concerns, gather feedback, and ensure their perspectives are considered.
- **Communicating and raising awareness of your project:** Developing engagement and communication plans that can support project managers create clear and consistent messaging about the project's purpose, goals, and benefits.
- **Managing Expectations:** Setting realistic expectations for stakeholders regarding project outcomes, timelines, and potential disruptions by addressing concerns, clarify misconceptions, and managing expectations.
- **Ensuring change readiness:** Assessing the readiness of an organisation or team for change and developing strategies to bridge any gaps.
- **Mitigating Risks:** Through anticipating and addressing risks associated with change, such as resistance, lack of stakeholder support, or unexpected obstacles.
- **Adopting change sustainably:** Supporting project managers in developing strategies to embed the changes into the organisation's culture, processes, and systems.



When would be the best time to start thinking about Change Management?

Answer:

Now!

[Click here for an introduction to Change Management](#)

[Click here to start exploring the Change Phases](#)

[Click here to access the Change Management Group](#)

